

# Architectural Services

## Asbestos Management

### Radcliffe Market Hall – Asbestos Management Plan Review



| Duty Holder/Responsible Person            | Developed with assistance from                                                                 | Original Issue date            |
|-------------------------------------------|------------------------------------------------------------------------------------------------|--------------------------------|
| Alan Mackrell<br>Manager<br>0161 249 2723 | Dave Winterbottom<br>Asbestos Surveyor<br>Premises Management<br>Bury Council<br>0161 253 6617 | 9 <sup>th</sup> September 2015 |
|                                           |                                                                                                | Last Review Date               |
|                                           |                                                                                                | 16 <sup>th</sup> June 2020     |
|                                           |                                                                                                | Next Review Date               |
|                                           |                                                                                                | June 2021                      |

This asbestos management plan has been facilitated by the Premises Management Section at Bury Council. Significant input was provided by Craig Allen who is the duty holder and who has an in-depth knowledge and understanding of the building use and activities carried out at the premises. A review of the management plan and an inspection to monitor the condition of the ACMs will be carried out at regular intervals. The results of this review are presented in appendixes D, E and F

## Table of Contents:

|                                                                                                         |    |
|---------------------------------------------------------------------------------------------------------|----|
| Introduction: .....                                                                                     | 1  |
| Responsibilities .....                                                                                  | 1  |
| Summary of Asbestos Containing Materials with Traffic Light System Showing<br>Priority for Action ..... | 2  |
| Site Plans .....                                                                                        | 3  |
| Asbestos Register and Action Plan .....                                                                 | 5  |
| Communication Plan .....                                                                                | 7  |
| Appendix A - Contractor Log .....                                                                       | 8  |
| Appendix B - Photographic Report .....                                                                  | 9  |
| Appendix C - Emergency Procedures .....                                                                 | 16 |
| Appendix D - Review .....                                                                               | 17 |
| Appendix E - AMP - Review Form .....                                                                    | 18 |
| Appendix F – Details of the Inspection to Monitor the Condition of the ACMs<br>insitu .....             | 19 |
| Appendix G - Asbestos Risk Assessment Methodology – Taken from HSG227 20                                |    |
| Appendix H – Asbestos Management Plan Implementation form – Staff Log ...                               | 25 |

## **Introduction:**

In recognition of its duties under Regulation 4 of the Control of Asbestos Regulations 2012, Bury Market Management has implemented the following asbestos management plan. The purpose of this management plan is to prevent exposure of pupils, staff and visitors, including contractors, to airborne asbestos fibres.

## **Responsibilities:**

### **Duty Holder/Responsible Person – Alan Mackrell –Manager**

Will be familiar with the location and condition of asbestos within these buildings and take this into consideration when commissioning refurbishment, repairs or general maintenance work. He will assist with the development and future review of this asbestos management plan to ensure that staff, visitors and the general public are not exposed to asbestos fibres. He will authorise payment for removals, surveys and time charges. He will provide access to all areas of the building for the purposes of identifying and monitoring ACMs and assist the asbestos surveyor by giving details of maintenance activities and building use for the Priority Risk Assessment. He will report accidental damage of ACMs to the authority's asbestos surveyor immediately. He will attend the premises hazards training course as required. He will stop any work where suspected asbestos is uncovered and seek advice from the authorities Asbestos Surveyor before continuing. He will ensure that a refurbishment and demolition asbestos survey is carried out prior to refurbishments. He must read updated management plans and refurbishment and demolition asbestos survey reports when they are issued and act on the report recommendations. If any areas of 'No Access' are identified the duty holder is responsible for ensuring they are accessed and inspected by a competent asbestos surveyor. He will ensure staff and contractors follow the procedures outlined in this document.

### **Staff**

The Health and Safety at Work Act places duties on employees for health and safety towards themselves and others. Market staff could potentially disturb ACMs causing dangerous fibre release and should, therefore, be familiar with the asbestos register and the position and condition of ACMs within their workplace. Maintenance operations adjacent to or within close proximity to fibrous ACMs will need to be risk assessed and a safe methodology employed. They will report any accidental damage of ACMs to the Manager. They will be required to attend premises hazard awareness courses as required. They will assist the Manager /asbestos surveyor with the priority risk assessment giving details of maintenance activities and building use. Staff will complete and sign the form in appendix H to confirm they have reviewed and understood the asbestos management plan.

### **Contractors**

All contractors undertaking work at the site that could potentially be exposed to ACMs will be asbestos awareness trained as a minimum. A copy of the site specific asbestos management plan will be reviewed by the contractor and operatives prior to any work being carried out. The contractors will complete and sign the form in appendix A to confirm they have reviewed and understood the asbestos management plan.

## Summary of Asbestos Containing Materials with Traffic Light System Showing Priority for Action

The risk assessment score was calculated using the methodology described in HSG227; see appendix F.

| Indoor Market Hall |          |                                                                     |
|--------------------|----------|---------------------------------------------------------------------|
| Item no.           | RA Score | Description/Comments                                                |
| 001                | -        | Cement wall cladding behind the door                                |
| 002                | -        | Internal seals and/ or components within the fuse boxes             |
| 003                | 9        | Cement cladding to walls                                            |
| 004                | -        | High level vertical cement panelling to stalls 8 – 16               |
| 005                | -        | Cement panelling including boxwork to ceiling                       |
| 006                | -        | Bitumen pads to underside of sink unit                              |
| 007                | 9        | Gaskets to pipework                                                 |
| 008                | 9        | Cement infill panel to ceiling                                      |
| 009                | 9        | Gaskets to pipework                                                 |
| 010                | 7        | Cement flue pipe emerging from wall at high level                   |
| 011                | 13       | Vertical cement panelling above the doorway leading to the external |

|               |                                                                 |
|---------------|-----------------------------------------------------------------|
| <b>Red</b>    | Represents urgent remedial/removal works                        |
| <b>Orange</b> | Represents a medium level of urgency for remedial/removal works |
| <b>Green</b>  | Represents no urgent remedial/removal works required            |

### Monitoring Inspection Frequency Calculator


|                                                                      |                                                                                                            |            |           |
|----------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------|------------|-----------|
| <b>Lower Risk Premises</b><br>1 monitoring visit required per annum  | No high risk ACMs are present. Only composite and/or low risk ACMs are evident from the management survey. | <b>Yes</b> | <b>No</b> |
| <b>Higher Risk Premises</b><br>2 monitoring visit required per annum | High risk ACMs present.                                                                                    | <b>Yes</b> | <b>No</b> |


Perceived risk ratings are based on the findings of the asbestos management survey and subsequent management plan. If refurbishment and demolition asbestos surveys are carried out that identify high risk ACM, which are to remain insitu and not be removed as part of a refurbishment project and added to the register then the perceived risk rating would need to be re-assessed. Also, if asbestos removals take place and ACM's are removed then the perceived risk rating would need to be re-assessed.

|                                                                                                                                                       |            |           |
|-------------------------------------------------------------------------------------------------------------------------------------------------------|------------|-----------|
| Is there any information presented that would require the monitoring frequency to be increased/decreased or criteria changed from the standard matrix | <b>Yes</b> | <b>No</b> |
|                                                                                                                                                       |            |           |

These premises have been deemed **Lower Risk Premises** and therefore monitoring visits will be carried out **once per annum**.

Site Plans

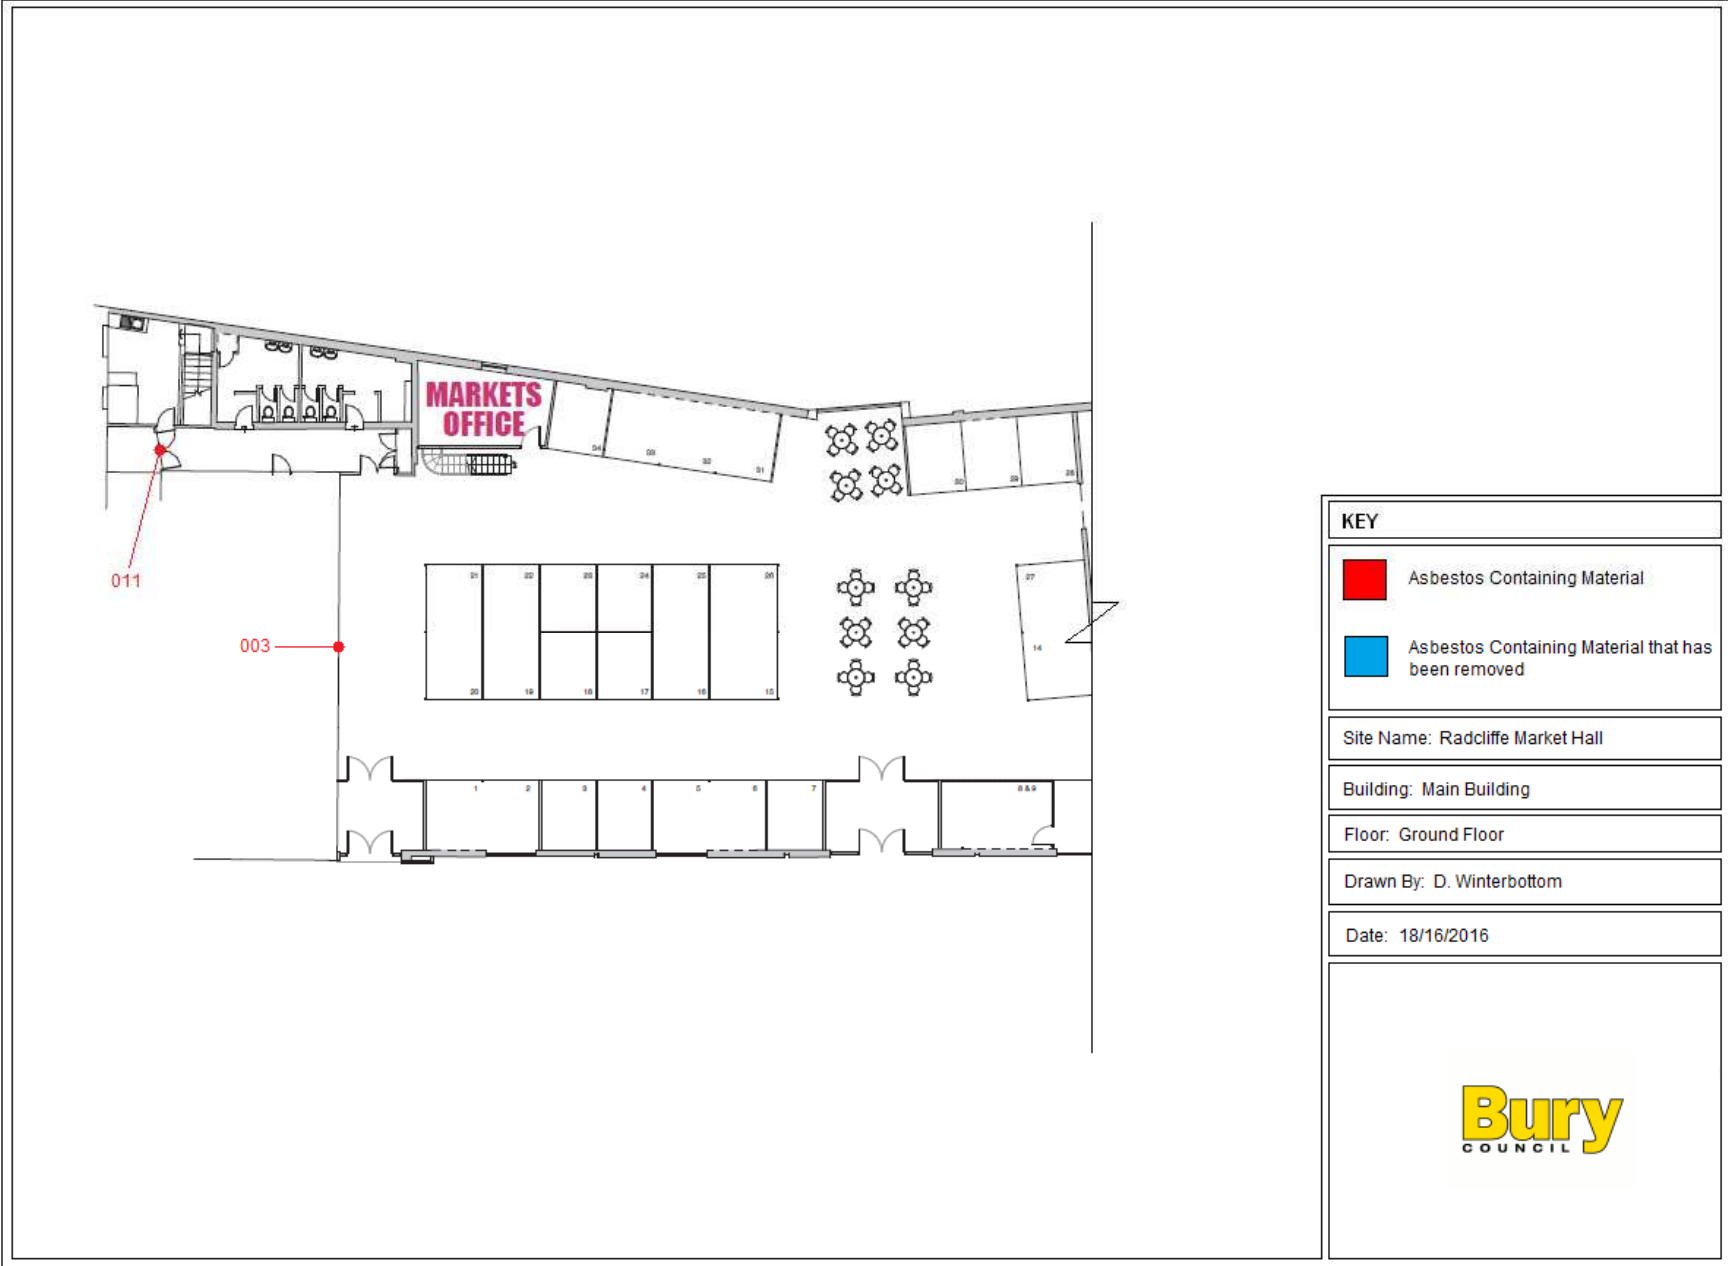

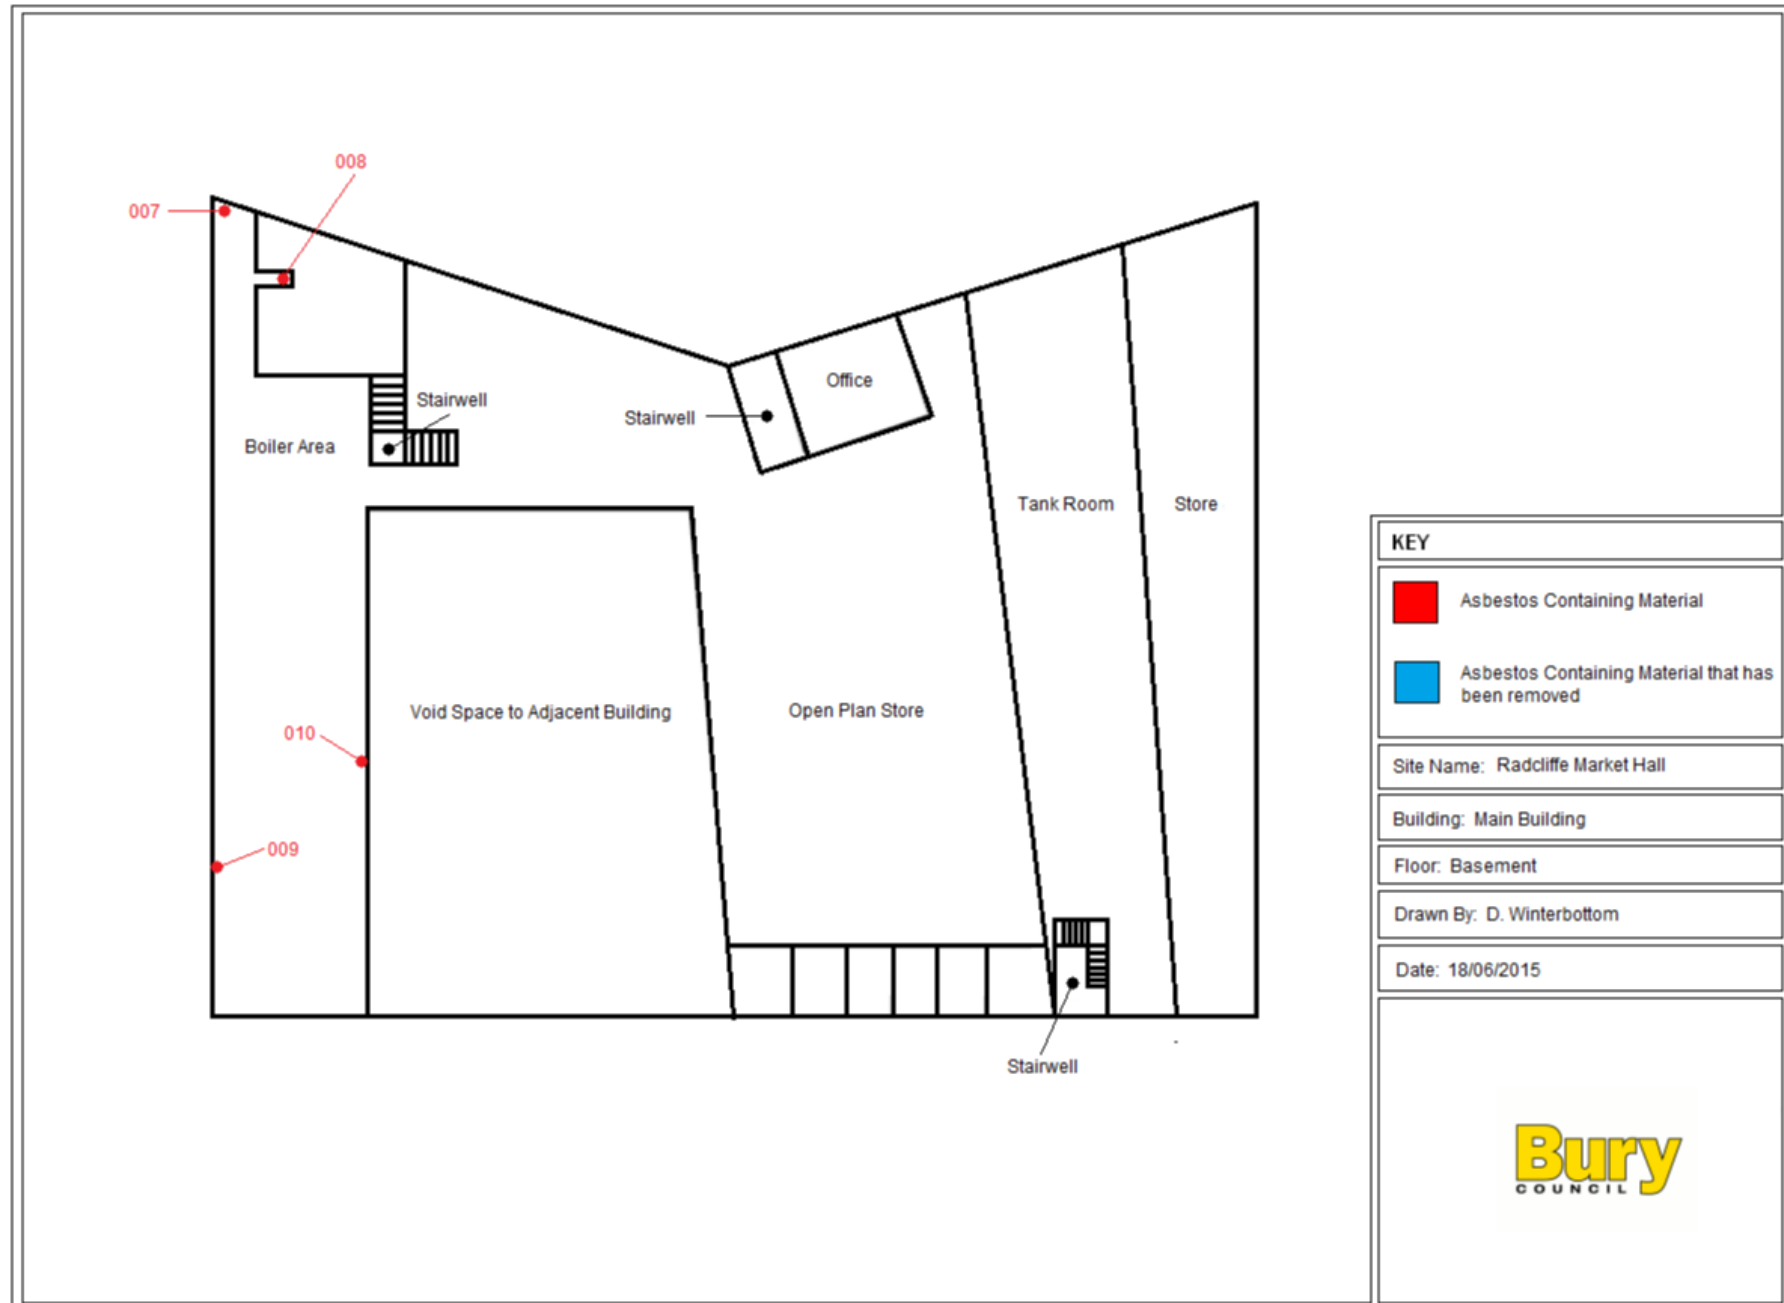

## Asbestos Register and Action Plan

| Item No   | Description                                            | Condition      | Surface Treatment | Asbestos Fibres Detected | Room/Area                               | Material Risk Score | Priority Risk Score | Risk Score | Next inspection date | Action/By whom/When                                                                                                                   | Extent                     |
|-----------|--------------------------------------------------------|----------------|-------------------|--------------------------|-----------------------------------------|---------------------|---------------------|------------|----------------------|---------------------------------------------------------------------------------------------------------------------------------------|----------------------------|
| 91-AI-001 | Cement wall cladding behind the door                   | Low Damage     | Cement            | Chrysotile               | 69/Electrics                            | 4                   | -                   | -          | 20/06/2016           | Item removed                                                                                                                          | 3m <sup>2</sup>            |
| 91-AI-002 | Internal seals and/or components within the fuse boxes | Undeterminable | Undeterminable    | Crocidolite              | 69/Electrics                            | 4-10                | -                   | -          | 20/06/2016           | Item removed                                                                                                                          | 11 no                      |
| 91-AI-003 | Cement cladding to walls                               | Low Damage     | Cement            | Chrysotile               | 72/Main Stall Area North East Elevation | 4                   | 5                   | 9          | June 2021            | Monitor condition & manage in-situ                                                                                                    | 30m <sup>2</sup>           |
| 91-AI-004 | High level vertical cement panelling to stalls 8 – 16  | Low Damage     | Cement            | Chrysotile               | Stalls 8-16                             | 4                   | -                   | -          | 20/06/2016           | Item removed                                                                                                                          | 50 Linear metre            |
| 91-AI-005 | Cement panelling including boxwork to ceiling          | Low Damage     | Cement            | Chrysotile               | Stalls 8-16                             | 4                   | -                   | -          | 20/06/2016           | Item removed                                                                                                                          | 10m <sup>2</sup> per stall |
| 91-AI-006 | Bitumen pads to underside of sink unit                 | Low Damage     | Composite         | Chrysotile               | Unit 67 Café                            | 3                   | -                   | -          | 20/06/2016           | Item removed                                                                                                                          | 2 no                       |
| 91-AI-007 | Gaskets to pipework                                    | Low Damage     | Unsealed gasket   | Chrysotile               | Boiler Area                             | 5                   | 4                   | 9          | June 2021            | Monitor condition & manage in-situ                                                                                                    | N/Q                        |
| 91-AI-008 | Cement infill panel to ceiling                         | Low Damage     | Cement            | Crocidolite Presumed     | Boiler Area                             | 6                   | 3                   | 9          | June 2021            | A sample should be taken by a competent person once safe access can be obtained. Until this occurs the item should be manage in situ. | 1m <sup>2</sup>            |
| 91-AI-009 | Gaskets to pipework                                    | Low Damage     | Unsealed gasket   | Chrysotile               | Boiler Area                             | 5                   | 4                   | 9          | June 2021            | Monitor condition & manage in-situ                                                                                                    | N/Q                        |

Architectural Services - Asbestos Management Plan – Radcliffe Market Hall

| Item No   | Description                                                         | Condition  | Surface Treatment | Asbestos Fibres Detected | Room/Area                | Material Risk Score | Priority Risk Score | Risk Score | Next inspection date | Action/By whom/When                                                                                                               | Extent          |
|-----------|---------------------------------------------------------------------|------------|-------------------|--------------------------|--------------------------|---------------------|---------------------|------------|----------------------|-----------------------------------------------------------------------------------------------------------------------------------|-----------------|
| 91-AI-010 | Cement flue pipe emerging from wall at high level                   | Low Damage | Cement            | Chrysotile               | Boiler Area              | 4                   | 3                   | 7          | June 2021            | Monitor condition & manage in-situ                                                                                                | 1 no            |
| 91-AI-011 | Vertical cement panelling above the doorway leading to the external | Low Damage | Cement            | Crocidolite Presumed     | Traders toilets corridor | 6                   | 7                   | 13         | June 2021            | A sample should be taken by a suitably trained competent person once the area is unoccupied until then monitor and manage in situ | 5m <sup>2</sup> |

\*A picture of each item is presented in the photographic report in appendix B. Item numbers in the building register above are taken from the last 3 numbers of the 'Asbestos Item ID' in the picture report.

## **Communication Plan**

### **Staff**

Operations personnel to review and be familiar with asbestos management plan and be aware of location and condition of ACMs.  
Report damage to ACMs to Alan Mackrell - Manager  
Staff and tenants to be informed of location of asbestos within their areas of use and report any damage to Alan Mackrell - Manager. Sign form in appendix H to confirm.  
Review AMP and sign form in appendix H.  
Take care when working adjacent to ACMs.  
Do not remove or work on any ACM.

### **Maintenance**

Review AMP and sign form (appendix A) prior to carrying out work.  
Take care when working adjacent to ACMs.  
Do not remove or work on any ACM.  
Be asbestos awareness trained.  
Contractors who regularly carryout work at the market hall will receive an electronic copy of the management plan (see below).  
Report damage to ACMs to Alan Mackrell - Manager

### **Contractors**

Review AMP and sign form prior to carrying out work.  
Contractors to be aware of asbestos in the buildings and in particular in the areas they are working in.  
Take care when working adjacent to ACMs.  
Do not remove or work on any ACM.  
Be asbestos awareness trained.  
Contractors who regularly carryout work at the market hall will receive an electronic copy of the management plan (see below).  
Report damage to ACMs to Alan Mackrell - Manager

### **Contractors – Regular contractors who carryout work for Market Management on a weekly basis**

There are a number of contractors who carryout regular work for the Market Management and can be onsite a couple of times a week. It is not practical for these contractors to review the asbestos management plan prior to each visit, so they will review the management plan and be familiar with the location and condition in the buildings they work in and sign the contractor log form following each issue of the reviewed asbestos management plan (every six months). They will receive an electronic copy of the asbestos management plan and subsequent updated management plans and each operative who regularly carries out work at the Market site will review the plan and sign the contractor log in appendix A. Any new operatives visiting site to carryout work will review the asbestos management plan and sign the contractor log in appendix A.  
Take care when working adjacent to ACMs.  
Do not remove or work on any ACM.  
Be asbestos awareness trained.  
Report damage to ACMs to Alan Mackrell - Manager

## Appendix A - Contractor Log

Each contractor supervisor must review the asbestos management plan with building register and sign this form. Copy this form and keep it with your report to record contractors coming on to site.

| Contractor/Company | Name of Operative | Brief Details of Works Undertaken and location | Date | I have read and understood the asbestos management plan including building register and my work will not disturb any ACMs |
|--------------------|-------------------|------------------------------------------------|------|---------------------------------------------------------------------------------------------------------------------------|
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |
|                    |                   |                                                |      | Sign:                                                                                                                     |

## **Appendix B - Photographic Report**

|                          |                                      |                                                                                    |                               |
|--------------------------|--------------------------------------|------------------------------------------------------------------------------------|-------------------------------|
| <b>Asb Item ID:</b>      | 91-AI-001                            |  |                               |
| <b>Item Description:</b> | Cement wall cladding behind the door |                                                                                    |                               |
| <b>Location:</b>         | 69/Electrics                         |                                                                                    |                               |
| <b>Asbestos Fibres:</b>  | Chrysotile                           |                                                                                    |                               |
| <b>HSE Notifiable:</b>   | No                                   |                                                                                    |                               |
| <b>Extent:</b>           | 3m2                                  |                                                                                    |                               |
| <b>Priority Rating:</b>  | Green                                |                                                                                    |                               |
| <b>Material Risk:</b>    | 4                                    |                                                                                    |                               |
| <b>Damage:</b>           | Low Damage                           |                                                                                    |                               |
| <b>Closure Notice:</b>   | No                                   |                                                                                    | <b>Photo Date:</b> 05/06/2009 |
| <b>Date Issued:</b>      |                                      |                                                                                    |                               |
| <b>Date Corrected:</b>   |                                      |                                                                                    |                               |
| <b>Recommendation</b>    | Item removed                         |                                                                                    |                               |

|                          |                                                         |                                                                                      |                               |
|--------------------------|---------------------------------------------------------|--------------------------------------------------------------------------------------|-------------------------------|
| <b>Asb Item ID:</b>      | 91-AI-002                                               |  |                               |
| <b>Item Description:</b> | Internal seals and/ or components within the fuse boxes |                                                                                      |                               |
| <b>Location:</b>         | 69/Electrics                                            |                                                                                      |                               |
| <b>Asbestos Fibres:</b>  | Crocidolite                                             |                                                                                      |                               |
| <b>HSE Notifiable:</b>   | Undeterminable                                          |                                                                                      |                               |
| <b>Extent:</b>           | 11 no                                                   |                                                                                      |                               |
| <b>Priority Rating:</b>  | Green                                                   |                                                                                      |                               |
| <b>Material Risk:</b>    | 4-10                                                    |                                                                                      |                               |
| <b>Damage:</b>           | Undeterminable                                          |                                                                                      |                               |
| <b>Closure Notice:</b>   | No                                                      |                                                                                      | <b>Photo Date:</b> 05/06/2009 |
| <b>Date Issued:</b>      |                                                         |                                                                                      |                               |
| <b>Date Corrected:</b>   |                                                         |                                                                                      |                               |
| <b>Recommendation</b>    | Item removed                                            |                                                                                      |                               |

|                          |                                         |                                                                                    |
|--------------------------|-----------------------------------------|------------------------------------------------------------------------------------|
| <b>Asb Item ID:</b>      | 91-AI-003                               |  |
| <b>Item Description:</b> | Cement cladding to walls                |                                                                                    |
| <b>Location:</b>         | 72/Main Stall Area North East Elevation |                                                                                    |
| <b>Asbestos Fibres:</b>  | Chrysotile                              |                                                                                    |
| <b>HSE Notifiable:</b>   | No                                      |                                                                                    |
| <b>Extent:</b>           | 30m2                                    |                                                                                    |
| <b>Priority Rating:</b>  | Green                                   |                                                                                    |
| <b>Material Risk:</b>    | 4                                       |                                                                                    |
| <b>Damage:</b>           | Low Damage                              |                                                                                    |
| <b>Closure Notice:</b>   | No                                      |                                                                                    |
| <b>Date Issued:</b>      |                                         | <b>Photo Date:</b> 26/06/2015                                                      |
| <b>Date Corrected:</b>   |                                         |                                                                                    |
| <b>Recommendation</b>    | Monitor condition & manage in-situ      |                                                                                    |

|                          |                                                       |                                                                                      |
|--------------------------|-------------------------------------------------------|--------------------------------------------------------------------------------------|
| <b>Asb Item ID:</b>      | 91-AI-004                                             |  |
| <b>Item Description:</b> | High level vertical cement panelling to stalls 8 - 16 |                                                                                      |
| <b>Location:</b>         | Stalls 8-16                                           |                                                                                      |
| <b>Asbestos Fibres:</b>  | Chrysotile                                            |                                                                                      |
| <b>HSE Notifiable:</b>   | No                                                    |                                                                                      |
| <b>Extent:</b>           | 50 Linear metre                                       |                                                                                      |
| <b>Priority Rating:</b>  | Green                                                 |                                                                                      |
| <b>Material Risk:</b>    | 4                                                     |                                                                                      |
| <b>Damage:</b>           | Low Damage                                            |                                                                                      |
| <b>Closure Notice:</b>   | No                                                    |                                                                                      |
| <b>Date Issued:</b>      |                                                       | <b>Photo Date:</b> 05/06/2009                                                        |
| <b>Date Corrected:</b>   |                                                       |                                                                                      |
| <b>Recommendation</b>    | Item removed                                          |                                                                                      |

THIS ITEM HAS NOW BEEN REMOVED

Architectural Services - Asbestos Management Plan – Radcliffe Market Hall

|                          |                                               |                                                                                                                          |
|--------------------------|-----------------------------------------------|--------------------------------------------------------------------------------------------------------------------------|
| <b>Asb Item ID:</b>      | 91-AI-005                                     |                                        |
| <b>Item Description:</b> | Cement panelling including boxwork to ceiling |                                                                                                                          |
| <b>Location:</b>         | Stalls 8-16                                   |                                                                                                                          |
| <b>Asbestos Fibres:</b>  | Chrysotile                                    |                                                                                                                          |
| <b>HSE Notifiable:</b>   | No                                            |                                                                                                                          |
| <b>Extent:</b>           | 10m2 per stall                                |                                                                                                                          |
| <b>Priority Rating:</b>  | Green                                         |                                                                                                                          |
| <b>Material Risk:</b>    | 4                                             |                                                                                                                          |
| <b>Damage:</b>           | Low Damage                                    |                                                                                                                          |
| <b>Closure Notice:</b>   | No                                            |                                                                                                                          |
| <b>Date Issued:</b>      |                                               | <div style="border: 1px solid black; padding: 5px; display: inline-block;"> <b>Photo Date:</b> 05/06/2009         </div> |
| <b>Date Corrected:</b>   |                                               |                                                                                                                          |
| <b>Recommendation</b>    | Item removed                                  |                                                                                                                          |

THIS ITEM HAS NOW BEEN REMOVED

|                          |                                        |                                                                                                                          |
|--------------------------|----------------------------------------|--------------------------------------------------------------------------------------------------------------------------|
| <b>Asb Item ID:</b>      | 91-AI-006                              |                                      |
| <b>Item Description:</b> | Bitumen pads to underside of sink unit |                                                                                                                          |
| <b>Location:</b>         | Unit 67 Café                           |                                                                                                                          |
| <b>Asbestos Fibres:</b>  | Chrysotile                             |                                                                                                                          |
| <b>HSE Notifiable:</b>   | No                                     |                                                                                                                          |
| <b>Extent:</b>           | 2 no                                   |                                                                                                                          |
| <b>Priority Rating:</b>  | Green                                  |                                                                                                                          |
| <b>Material Risk:</b>    | 3                                      |                                                                                                                          |
| <b>Damage:</b>           | Low Damage                             |                                                                                                                          |
| <b>Closure Notice:</b>   | No                                     |                                                                                                                          |
| <b>Date Issued:</b>      |                                        | <div style="border: 1px solid black; padding: 5px; display: inline-block;"> <b>Photo Date:</b> 05/06/2009         </div> |
| <b>Date Corrected:</b>   |                                        |                                                                                                                          |
| <b>Recommendation</b>    | Item removed                           |                                                                                                                          |

THIS ITEM HAS NOW BEEN REMOVED

Architectural Services - Asbestos Management Plan – Radcliffe Market Hall

|                          |                                    |                                                                                    |
|--------------------------|------------------------------------|------------------------------------------------------------------------------------|
| <b>Asb Item ID:</b>      | 91-AI-007                          |  |
| <b>Item Description:</b> | Gaskets to pipework                |                                                                                    |
| <b>Location:</b>         | Boiler Area                        |                                                                                    |
| <b>Asbestos Fibres:</b>  | Chrysotile                         |                                                                                    |
| <b>HSE Notifiable:</b>   | No                                 |                                                                                    |
| <b>Extent:</b>           | N/Q                                |                                                                                    |
| <b>Priority Rating:</b>  | Green                              |                                                                                    |
| <b>Material Risk:</b>    | 5                                  |                                                                                    |
| <b>Damage:</b>           | Low Damage                         |                                                                                    |
| <b>Closure Notice:</b>   | No                                 |                                                                                    |
| <b>Date Issued:</b>      |                                    | <b>Photo Date:</b> 05/06/2009                                                      |
| <b>Date Corrected:</b>   |                                    |                                                                                    |
| <b>Recommendation</b>    | Monitor condition & manage in-situ |                                                                                    |

|                          |                                                                                                                                       |                                                                                      |
|--------------------------|---------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------|
| <b>Asb Item ID:</b>      | 91-AI-008                                                                                                                             |  |
| <b>Item Description:</b> | Cement infill panel to ceiling                                                                                                        |                                                                                      |
| <b>Location:</b>         | Boiler Area                                                                                                                           |                                                                                      |
| <b>Asbestos Fibres:</b>  | Crocidolite Presumed                                                                                                                  |                                                                                      |
| <b>HSE Notifiable:</b>   | No                                                                                                                                    |                                                                                      |
| <b>Extent:</b>           | 1m2                                                                                                                                   |                                                                                      |
| <b>Priority Rating:</b>  | Green                                                                                                                                 |                                                                                      |
| <b>Material Risk:</b>    | 6                                                                                                                                     |                                                                                      |
| <b>Damage:</b>           | Low Damage                                                                                                                            |                                                                                      |
| <b>Closure Notice:</b>   | No                                                                                                                                    |                                                                                      |
| <b>Date Issued:</b>      |                                                                                                                                       | <b>Photo Date:</b> 05/06/2009                                                        |
| <b>Date Corrected:</b>   |                                                                                                                                       |                                                                                      |
| <b>Recommendation</b>    | A sample should be taken by a competent person once safe access can be obtained. Until this occurs the item should be manage in situ. |                                                                                      |


Architectural Services - Asbestos Management Plan – Radcliffe Market Hall

|                          |                                    |                                                                                    |
|--------------------------|------------------------------------|------------------------------------------------------------------------------------|
| <b>Asb Item ID:</b>      | 91-AI-009                          |  |
| <b>Item Description:</b> | Gaskets to pipework                |                                                                                    |
| <b>Location:</b>         | Boiler Area                        |                                                                                    |
| <b>Asbestos Fibres:</b>  | Chrysotile                         |                                                                                    |
| <b>HSE Notifiable:</b>   | No                                 |                                                                                    |
| <b>Extent:</b>           | N/Q                                |                                                                                    |
| <b>Priority Rating:</b>  | Green                              |                                                                                    |
| <b>Material Risk:</b>    | 5                                  |                                                                                    |
| <b>Damage:</b>           | Low Damage                         |                                                                                    |
| <b>Closure Notice:</b>   | No                                 |                                                                                    |
| <b>Date Issued:</b>      |                                    | <b>Photo Date:</b> 05/06/2009                                                      |
| <b>Date Corrected:</b>   |                                    |                                                                                    |
| <b>Recommendation</b>    | Monitor condition & manage in-situ |                                                                                    |

|                          |                                                   |                                                                                      |
|--------------------------|---------------------------------------------------|--------------------------------------------------------------------------------------|
| <b>Asb Item ID:</b>      | 91-AI-010                                         |  |
| <b>Item Description:</b> | Cement flue pipe emerging from wall at high level |                                                                                      |
| <b>Location:</b>         | Boiler Area                                       |                                                                                      |
| <b>Asbestos Fibres:</b>  | Chrysotile                                        |                                                                                      |
| <b>HSE Notifiable:</b>   | No                                                |                                                                                      |
| <b>Extent:</b>           | 1 no                                              |                                                                                      |
| <b>Priority Rating:</b>  | Green                                             |                                                                                      |
| <b>Material Risk:</b>    | 4                                                 |                                                                                      |
| <b>Damage:</b>           | Low Damage                                        |                                                                                      |
| <b>Closure Notice:</b>   | No                                                |                                                                                      |
| <b>Date Issued:</b>      |                                                   | <b>Photo Date:</b> 26/06/2015                                                        |
| <b>Date Corrected:</b>   |                                                   |                                                                                      |
| <b>Recommendation</b>    | Monitor condition & manage in-situ                |                                                                                      |

|                          |                                                                                                                                   |                                                                                    |            |
|--------------------------|-----------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------|------------|
| <b>Asb Item ID:</b>      | 91-AI-011                                                                                                                         |  |            |
| <b>Item Description:</b> | Vertical cement panelling above the doorway leading to the external                                                               |                                                                                    |            |
| <b>Location:</b>         | Traders toilets corridor                                                                                                          |                                                                                    |            |
| <b>Asbestos Fibres:</b>  | Crocidolite Presumed                                                                                                              |                                                                                    |            |
| <b>HSE Notifiable:</b>   | No                                                                                                                                |                                                                                    |            |
| <b>Extent:</b>           | 5m2                                                                                                                               |                                                                                    |            |
| <b>Priority Rating:</b>  | Green                                                                                                                             |                                                                                    |            |
| <b>Material Risk:</b>    | 6                                                                                                                                 |                                                                                    |            |
| <b>Damage:</b>           | Low Damage                                                                                                                        |                                                                                    |            |
| <b>Closure Notice:</b>   | No                                                                                                                                |                                                                                    |            |
| <b>Date Issued:</b>      |                                                                                                                                   | <b>Photo Date:</b>                                                                 | 26/06/2015 |
| <b>Date Corrected:</b>   |                                                                                                                                   |                                                                                    |            |
| <b>Recommendation</b>    | A sample should be taken by a suitably trained competent person once the area is unoccupied until then monitor and manage in situ |                                                                                    |            |

## Appendix C - Emergency Procedures

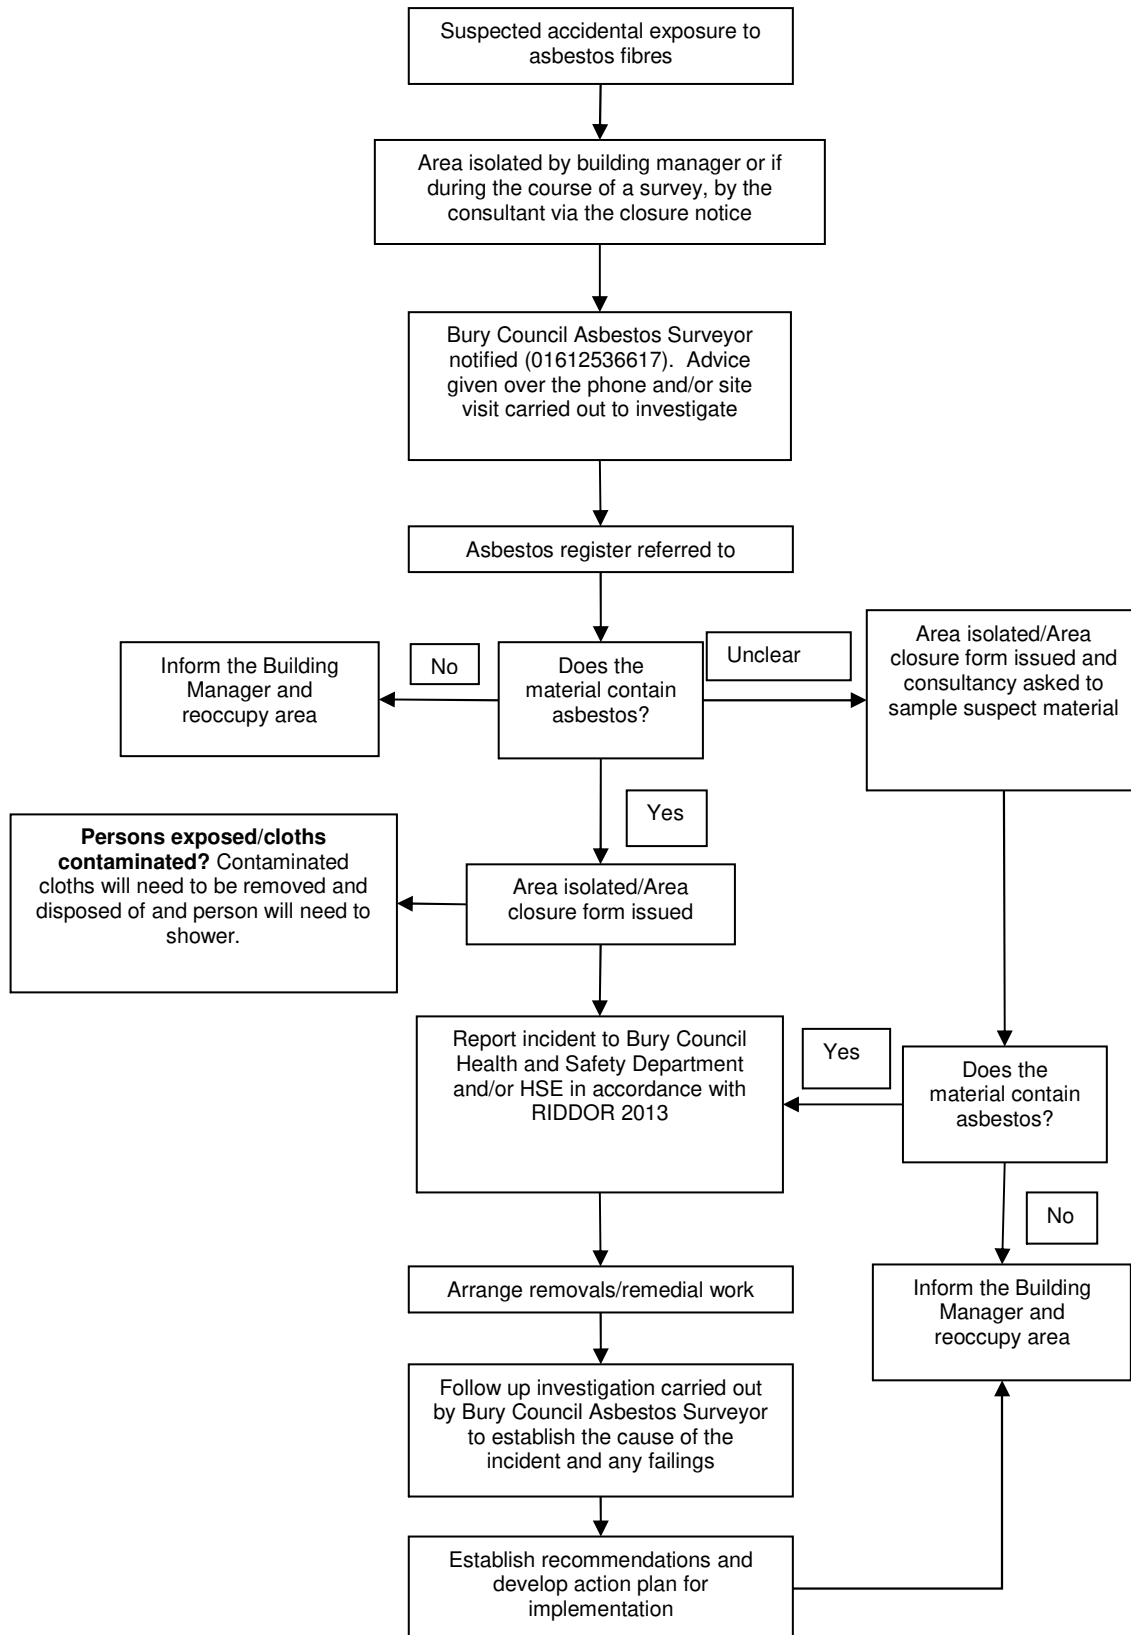

## Appendix D - Review

[illegible]

## Appendix E - AMP - Review Form

# Architectural Services Asbestos Management Asbestos Management Plan Review Form

| Site Name             | Site ID |
|-----------------------|---------|
| Radcliffe Market Hall | 91      |

| Review Carried Out By |                             | Date       |
|-----------------------|-----------------------------|------------|
| Name                  | Position                    | 16/06/2020 |
| S.Osullivan           | Director                    |            |
| A.Skinner             | Contracts/Asbestos Surveyor |            |

|                                                                                     |     |
|-------------------------------------------------------------------------------------|-----|
| Has the condition of ACMs changed?                                                  | No  |
| Details:                                                                            |     |
|                                                                                     |     |
| Does this require any remedial action to be carried out?                            | No  |
| Details:                                                                            |     |
|                                                                                     |     |
| Have there been any incidents of accidental ACM disturbance?                        | No  |
| Details:                                                                            |     |
|                                                                                     |     |
| Was the disturbance or suspected disturbance dealt with safely?                     | N/A |
| Details:                                                                            |     |
|                                                                                     |     |
| Have contractors been reviewing the AMP and signing the contractor log?             | Yes |
| If no, what action is required to ensure the procedure is implemented and followed? |     |
|                                                                                     |     |
| Are any other changes required to the AMP other than those above?                   | No  |
| Details:                                                                            |     |
|                                                                                     |     |

## **Appendix F – Details of the Inspection to Monitor the Condition of the ACMs insitu**

### **Introduction**

An asbestos condition survey was carried out by Bury Council Architectural Services on the 16<sup>th</sup> June 2020 to inspect the condition of identified and presumed asbestos containing materials discovered during the last asbestos management survey AS1366 carried out by LK Assure Ltd on 05/06/2009.

### **Inspection Summary**

The following asbestos items have changed condition since the last inspection:

All items are in the same condition as previously noted.

**PLEASE ACT ON THE RECOMMENDATIONS IN THE ASBESTOS REGISTER AND ACTION PLAN SECTION OF THIS MANAGEMENT PLAN.**

The following asbestos items could not be re-inspected during this survey:

All items inspected.

The condition of the asbestos containing materials will be re-assessed in June 2021.

### **Additional Information and Guidance**

This updated asbestos management plan is issued to replace your initial asbestos management plan and to assist the duty holder in their compliance with the requirements under regulation 4 (8), (9) & (10) of the Control of Asbestos Regulation 2012.

The initial asbestos management plan provided information on non-asbestos items, no access areas, caveats to the original survey, the survey methodology, the sampling certificates of analysis and terminology definitions. Where applicable, this information is included within this report in the appendices.

Previous asbestos management plans issued by Bury Council can be discarded or archived following receipt of this report. Historical reports are kept by the Premises Management Section of Bury Council.

## Appendix G - Asbestos Risk Assessment Methodology – Taken from HSG227

### Material assessment and algorithm

***The risk assessment includes a material assessment and a priority assessment.***

***The material assessment looks at the type and condition of the ACM and the ease with which it will release fibres if disturbed.***

***The priority assessment (appendix 3) looks at the likelihood of someone disturbing the ACM.***

8 The material assessment is an assessment of the condition of the ACM, or the presumed ACM, and the likelihood of it releasing fibres in the event of it being disturbed in some way. This material assessment will give a good initial guide to the priority for management as it will identify the materials which will most readily release airborne fibres if disturbed. However, there are other factors to take into account when prioritising action. These are considered in the priority assessment which is described in Appendix 3.

9 MDHS100<sup>13</sup> recommends the use of an algorithm to carry out the material assessment, and contains an example. The algorithm is a numerical way of taking into account several influencing factors, giving each factor considered a score. These scores can then be totaled to give a material assessment score. The use of algorithms is not infallible, but the assessment process is clear for all to see, so if discrepancies arise, it should be possible to track back through the assessment process to find the root of the error. The algorithm shown in MDHS100<sup>13</sup> considers four parameters that determine the risk from an ACM: that is the ability to release fibres if disturbed. These four parameters are:

- product type;
- extent of damage;
- surface treatment; and
- asbestos type.

10 Each of the parameters is scored and added to give a total score between 2 and 12:

- materials with scores of 10 or more should be regarded as high risk with a significant potential to release fibres if disturbed;
- those with a score between 7 and 9 are regarded as medium risk;
- materials with a score between 5 and 6 are low risk; and
- scores of 4 or less are very low risk.

11 The material assessment algorithm shown in MDHS100<sup>13</sup> is reproduced here. You should now read on to the priority assessment in Appendix 3.

**Table 2** Material assessment algorithm

| Sample variable                          | Score | Examples of scores                                                                                                                                          |
|------------------------------------------|-------|-------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Product type<br>(or debris from product) | 1     | Asbestos reinforced composites (plastics, resins, mastics, roofing felts, vinyl floor tiles, semi-rigid paints or decorative finishes, asbestos cement etc) |
|                                          | 2     | Asbestos insulating board, mill boards, other low density insulation boards, asbestos textiles, gaskets, ropes and woven textiles, asbestos paper and felt  |
|                                          | 3     | Thermal insulation (eg pipe and boiler lagging), sprayed asbestos, loose asbestos, asbestos mattresses and packing                                          |
| Extent of damage/<br>deterioration       | 0     | Good condition: no visible damage                                                                                                                           |
|                                          | 1     | Low damage: a few scratches or surface marks; broken edges on boards, tiles etc                                                                             |
|                                          | 2     | Medium damage: significant breakage of materials or several small areas where material has been damaged revealing loose asbestos fibres                     |
|                                          | 3     | High damage or delamination of materials, sprays and thermal insulation. Visible asbestos debris                                                            |
| Surface treatment                        | 0     | Composite materials containing asbestos: reinforced plastics, resins, vinyl tiles                                                                           |
|                                          | 1     | Enclosed sprays and lagging, asbestos insulating board (with exposed face painted or encapsulated), asbestos cement sheets etc                              |
|                                          | 2     | Unsealed asbestos insulating board, or encapsulated lagging and sprays                                                                                      |
|                                          | 3     | Unsealed laggings and sprays                                                                                                                                |
| Asbestos type                            | 1     | Chrysotile                                                                                                                                                  |
|                                          | 2     | Amphibole asbestos excluding crocidolite                                                                                                                    |
|                                          | 3     | Crocidolite                                                                                                                                                 |
| Total score                              |       |                                                                                                                                                             |

## PRIORITY ASSESSMENT AND ALGORITHM

1 The material assessment (see Appendix 2) identifies the high risk materials, that is, those which will most readily release airborne fibres if disturbed. It does not automatically follow that those materials assigned the highest score in the material assessment will be the materials that should be given priority for remedial action. Management priority must be determined by carrying out a risk assessment which will also take into account factors such as:

- maintenance activity;
- occupant activity;
- likelihood of disturbance;
- human exposure potential.

***The risk assessment includes a material assessment and a priority assessment.***

***The material assessment (appendix 2) looks at the type and condition of the ACM and the ease with which it will release fibres if disturbed.***

***The priority assessment looks at the likelihood of someone disturbing the ACM.***

2 The risk assessment can only be carried out with detailed knowledge of all the above. Although a surveyor may have some of the information which will contribute to the risk assessment and may be part of an assessment team, you, as the duty holder under CAW,<sup>5</sup> are required to make the risk assessment, using the information given in the survey report and your detailed knowledge of the activities carried out within your premises. The risk assessment will form the basis of the management plan, so it is important that it is accurate.

### **Maintenance activity**

3 The first and most important factor which must be taken into consideration is the level of maintenance activity likely to be taking place in an area. Maintenance trades such as plumbers and electricians are the group who the duty to manage is primarily trying to protect. There are two types of maintenance activity, planned and unplanned. Planned work can be assessed and carried out using procedures and controls to reduce exposure to asbestos. Unplanned work requires the situation to be dealt with as found and the controls that can be applied may be more limited. The frequency of maintenance activities also need to be taken into account in deciding what management action is appropriate.

### **Occupant activity**

4 The activities carried out in an area will have an impact on the risk assessment. When carrying out a risk assessment the main type of use of an area and the activities taking place within it should be taken into account. For example a little used storeroom, or an attic, will rarely be accessed and so any asbestos is unlikely to be disturbed. At the other end of the scale, in a warehouse lined with asbestos insulating board panels, with frequent vehicular movements, the potential for disturbance of ACMs is reasonably high and this would be a significant factor in the risk assessment. As well as the normal everyday activities taking place in an area, any secondary activities will need to be taken into account.

### **Likelihood of disturbance**

5 The two factors that will determine the likelihood of disturbance are the extent or amount of the ACM and its accessibility/vulnerability. For example, asbestos soffits outdoors are generally

inaccessible without the use of ladders or scaffolding, are unlikely to be disturbed. The asbestos cement roof of a hospital ward is also unlikely to be disturbed, but its extent would need to be taken into account in any risk assessment. However if the same ward had asbestos panels on the walls they would be much more likely to be disturbed by trolley/bed movements.

### ***Human exposure potential***

6 The human exposure potential depends on three factors: the number of occupants of an area, the frequency of use of the area, and the average time each area is in use. For example, a school boiler room is likely to be unoccupied, but may be visited daily for a few minutes. The potential for exposure is much less than say in a classroom lined with asbestos insulating board paneling, which is occupied daily for six hours by 30 pupils and a teacher.

### **Priority assessment algorithms**

7 Taking all these factors into account in a logical, consistent manner is difficult. Using an algorithm will help you to produce priority assessments that have taken the factors into account in a consistent way. An example of an algorithm for use in making the priority assessment is shown in Table 2. The number of factors relevant at any one site needs to be carefully considered, as the more factors included in an algorithm, the lower the influence of the most important risk factors becomes, and this may produce anomalies. For this reason it is recommended that the number of factors that are scored is limited to four, the same as the number of factors in the material assessment (Appendix 2). There is no single set of factors that can be recommended that will apply equally to all types of premises. *Therefore four general headings have been used and one or more factors can be taken into account and averaged under each heading to suit the circumstances.* If you choose to use more than one factor under a general heading, then average the scores under that heading, rounding up where necessary.

8 The scores from the material assessment (ie the condition of the ACM or presumed ACM) are added to the scores of the priority assessment (the likelihood of disturbance), to give the overall risk assessment. Risk assessment scores for different ACMs can then be compared to develop your action plan. In many circumstances the scores will be similar, making decisions more difficult. For example a boiler house with asbestos pipework insulation in poor condition may get the same or similar risk assessment score to an office with asbestos insulating board in reasonably good condition. This is simply because the ACM in the boiler house received a higher score than the ACM in the office because the ACM in the boiler house was in poor condition. However, the priority assessment for the office will get a higher score than the boiler house since the office is occupied more often. Add the scores together for the material and priority assessments, and you get similar scores. If this is the case then you may decide that the office needs doing first because it is used daily. On the other hand you may decide that the poor condition of the ACM in the boiler house means that it should be done first.

9 If the office was a classroom, the young age of the occupants may be a deciding factor. Appendix 4 contains worked examples that may help you. Algorithms are provided to help you, but they are best guesses and will often require you to make your own additional judgments.

**Table 3** Priority assessment algorithm (read page 60, paragraph 7 on score averaging before using this algorithm)

| Assessment factor                                                                                                         | Score                                                    | Examples of score variables                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |
|---------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Normal occupant activity</b><br>Main type of activity in area<br><br>Secondary activities for area                     | 0<br>1<br>2<br>3<br>As above                             | Rare disturbance activity (eg little used store room<br>Low disturbance activities (eg office type activity)<br>Periodic disturbance (eg industrial or vehicular activity which may contact ACMs)<br>High levels of disturbance, (eg fire door with asbestos insulating board sheet in constant use)<br>As above                                                                                                                                                                               |
| <b>Likelihood of disturbance</b><br>Location<br><br>Accessibility<br><br>Extent/amount                                    | 0<br>1<br>2<br>3<br>0<br>1<br>2<br>3<br>0<br>1<br>2<br>3 | Outdoors<br>Large rooms or well-ventilated areas<br>Rooms up to 100m <sup>2</sup><br>Confined spaces<br>Usually inaccessible or unlikely to be disturbed<br>Occasionally likely to be disturbed<br>Easily disturbed<br>Routinely disturbed<br>Small amounts or items (eg strings, gaskets)<br>≤10 m <sup>2</sup> or ≤10 m pipe run.<br>>10 m <sup>2</sup> to ≤50 m <sup>2</sup> or >10 m to ≤50 m pipe run<br>>50 m <sup>2</sup> or >50 m pipe run                                             |
| <b>Human exposure potential</b><br>Number of occupants<br><br>Frequency of use of area<br><br>Average time area is in use | 0<br>1<br>2<br>3<br>0<br>1<br>2<br>3<br>0<br>1<br>2<br>3 | None<br>1 to 3<br>4 to 10<br>>10<br>Infrequent<br>Monthly<br>Weekly<br>Daily<br><1 hour<br>>1 to <3 hours<br>>3 to <6 hours<br>>6 hours                                                                                                                                                                                                                                                                                                                                                        |
| <b>Maintenance activity</b><br>Type of maintenance activity<br><br>Frequency of maintenance activity                      | 0<br>1<br>2<br>3<br>0<br>1<br>2<br>3                     | Minor disturbance (eg possibility of contact when gaining access)<br>Low disturbance (eg changing light bulbs in asbestos insulating board ceiling)<br>Medium disturbance (eg lifting one or two asbestos insulating board ceiling tiles to access a valve)<br>High levels of disturbance (eg removing a number of asbestos insulating board ceiling tiles to replace a valve or for re-cabling)<br>ACM unlikely to be disturbed for maintenance<br>≤1 per year<br>>1 per year<br>>1 per month |

## Appendix H – Asbestos Management Plan Implementation form – Staff Log

| Staff Name & Position | Summary of Advice Received | I have read and understood the asbestos management plan including building register and understand my responsibilities |
|-----------------------|----------------------------|------------------------------------------------------------------------------------------------------------------------|
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
|                       |                            | Sign: _____ Date: _____                                                                                                |
