

BS 5837:2012

Arboricultural Method Statement

18th December 2025

Report No. 2524_AMS.02

Project: Cemetery Road

Authored by: Matthew Lally



ARBORICULTURAL METHOD STATEMENT

PROJECT

Cemetery Road

Ramsbottom

Bury

BLO 9PU

LALLY TREE MANAGEMENT LIMITED

32 Thirlmere Road

Urmston

Manchester

M41 8PP

[T] 07305 740120

[E] matt@lallytreemanagement.co.uk

[W] www.lallytreemanagement.co.uk

Company No. 15847606

DOCUMENT ISSUE RECORD

Date of Inspection	Surveyor	Report Version	Issue Date	Author
08.08.2025	Matthew Lally. FdSc MArborA	02	18.12.2025	Matthew Lally. FdSc MArborA

This report is the property of Lally Tree Management Limited. This report may only be reproduced or disclosed to third parties with express written consent from Lally Tree Management Limited.

All comments, conclusions and recommendations within this report are based on the information available to Lally Tree Management Limited at the time of investigation. Lally Tree Management Limited accepts no liability in cases where the provided information is found to be inaccurate or misleading or if additional information exists or becomes available.

CONTENTS

1. INTRODUCTION	1
1.1. Author Information & Report Purpose.....	1
2. GENERAL INFORMATION	1
2.1. Understanding Tree Roots and Damaging Factors	1
3. METHOD STATEMENT	2
3.1. Sequence of Events.....	2
3.2. Pre-commencement Site Meeting	2
3.3. Tree Works	3
3.4. Site Briefing	3
3.5. Protective Fencing.....	4
3.6. Cellular Confinement System	5
3.7. Additional Precautions Outside Fenced Areas.....	7
3.8. Demolition adjacent to Trees & RPAs	8
3.9. Site Monitoring.....	8
<i>Appendix I Tree Removal Plan & Tree Protection Plan</i>	
<i>Appendix II Auditable Site Monitoring</i>	

1. INTRODUCTION

1.1. Author Information & Report Purpose

- 1.1.1. My name is Matthew Lally (FdSc) and I have created this Arboricultural Method Statement to outline the required steps which must be implemented to successfully retain the trees we wish to retain without adversely affecting their safe useful life expectancy. The steps in this Method Statement must be followed and if there is any misunderstanding or difficulty with these steps then I must be contacted immediately to clarify any issues.
- 1.1.2. Failure to adhere to the recommendations outlined in this document could result in tree decline or tree death which will mean a breach of planning consent. The trees outlined for retention in this document are protected by planning law and any tree loss and damage could result in prosecution.

2. GENERAL INFORMATION

2.1. Understanding Tree Roots and Damaging Factors

- 2.1.1. It is important to understand that the majority of the root system is within the top 600mm of the soil extending radially for distances in excess of the Root Protection Area (the Root protection Area is simply the minimal amount of untouched root system deemed to be required for this tree to be successfully retained). Beyond the main structural roots (close to the base of the trunk), the root system rapidly sub-divides into smaller diameter roots: off this main system, a mass of fine roots develops which are incredibly important for the tree to be able to take up water and essential nutrients.
- 2.1.2. These very fine roots are easily damaged by a number of factors such as: -
- a) Compaction of the ground, which reduces the space between soil particles. This is particularly important on clay soils. A single passage by heavy equipment on clay soils or storage of heavy materials can cause significant damage.
 - b) Changing soil levels, even for a few weeks.
 - c) Covering the root area with impervious surfaces.
 - d) A rise in the level of the water table. Roots can tolerate submersion for short periods. But a permanent rise will deplete the soil of oxygen.

- e) Stripping the topsoil, such works must be avoided until protective fencing has been erected.
- f) Pollution, such as cement washings & oils.
- g) Excavations in the root protection area. Even shallow excavations can cause damage and therefore must be avoided unless otherwise stated in this document.

3. METHOD STATEMENT

3.1. Sequence of Events

- 3.1.1. I have compiled the sequence of events below that must be undertaken in the order stated. Each step listed below is then expanded upon in section 3.2 onwards to ensure the requirements for each step are understood. This sequence should be read in conjunction with the Tree Removal Plan & the Tree Protection Plan in appendix I.

- 1) Pre-commencement site meeting (See 3.2)
- 2) Tree pruning & removal (See 3.3)
- 3) Site briefing for personnel (See 3.4)
- 4) Installation of protective fencing (See 3.5)
- 5) Installation of cellular confinement system (3.6)

Steps 1 to 5 must be undertaken before any works begin onsite.

- 6) Implementation of development (See 3.7, 3.8, 3.9)
- 7) Completion of development works
- 8) Removal of protective fencing
- 9) Completion signed off

3.2. Pre-commencement Site Meeting

- 3.2.1. Prior to commencement of any site works or tree works, a meeting onsite must take place including the site manager and an arboricultural consultant. This meeting will allow further discussion of the programme of works, tree protective measures, locations of areas for storage/site organisation and the agreement of any changes to the Arboricultural Method Statement that may be required which will be formally updated and approved as required.

3.3. Tree Works

- 3.3.1. Once the pre-commencement site meeting has taken place then the following tree works must be undertaken by a qualified and insured tree surgery company.

Table 1. Table of tree works

Tree No.	Species	Proposed Works to Facilitate Development	Reason for Works
T1	Elderberry	No Works Required	-
T2	Holly	No Works Required	-
T3	Sycamore	No Works Required	-
T4	Holly	Reduce crown on the northwestern side by 1m as outlined in the Tree Removal Plan	To facilitate the construction of the building and erection of scaffolding
T5	Horse Chestnut	No Works Required	-
T6	Ash	No Works Required	-
T7	Cherry	Remove	To facilitate the construction
T8	Pedunculate oak	Reduce crown on the eastern side by 1.7m as outlined in the Tree Removal Plan. Crown lift to 4m	To aid the installation of scaffolding, to allow light into the property and reduce the amount of crown over the drive
T9	Sycamore	Remove	To facilitate the construction
G10	Holly	No Works Required	-
T11	Ash	No Works Required	-
T12#	Griselinia	No Works Required	-

All tree works must be undertaken in line with BS3998:2010. Tree Work. Recommendations.

3.4. Site Briefing

- 3.4.1. Once the tree works have been completed to the recommended specifications and standards outlined in section 3.3, the site manager must ensure that all personnel who are to be working on this site are made fully aware of the constraints posed by the retained trees and that there are measures in place to protect these trees. I recommend making sure that all personnel have full access to the Arboricultural Method Statement and Tree

Protection Plan (TPP), keeping a hard copy of this in the site office would also be advisable for reference.

3.5. Protective Fencing

- 3.5.1. Now that the site briefing has been completed, the protective fencing should be erected in the positions laid out in the Tree Protection Plan which I have made available in appendix I.
- 3.5.2. The tree protection fencing will be appropriate to the degree and proximity of likely construction works. It is my opinion that in this instance, the default BS 5837:2012 tree protection fencing is disproportionate. I recommend that (if acceptable by the LPA) an adequate level of protection for the trees could be provided by 'Heras' type fencing, of welded mesh panels on rubber or concrete feet., I have included an image of the compliant fencing available in figure 1.

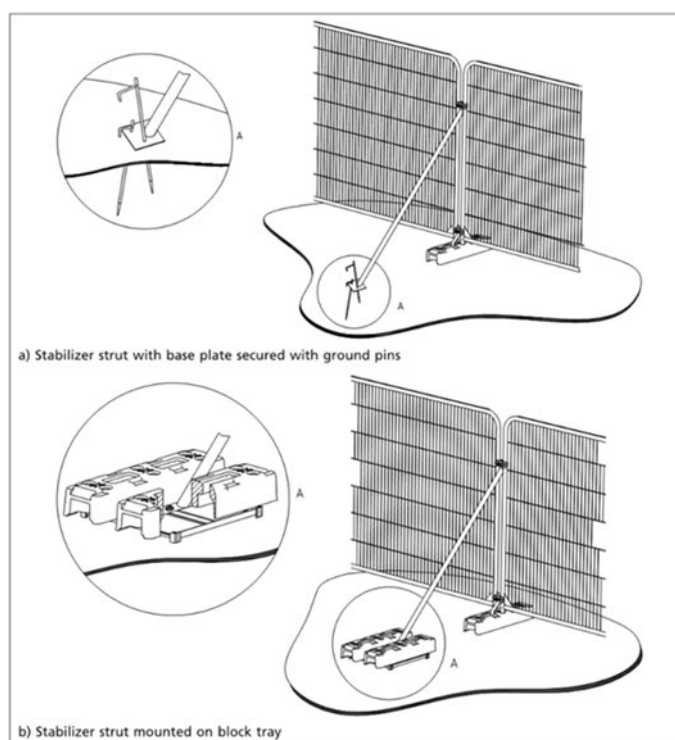


Figure 1. Tree protection fencing (Heras)

- 3.5.3. The fencing should be strong and suitable for local conditions. It should also take into account the degree of construction activity on the site.
- 3.5.4. Notices must also be erected on the fencing stating, 'Protected Area - No operations within fenced area'. I have made an example of a notice sign available in figure 2.



Figure 2. Tree protection notice to be fixed to protective fencing

- 3.5.5. Once the fence has been erected it should never be crossed and particular care should be taken not to store any materials or soil within the protected area.

3.6. Cellular Confinement System

- 3.6.1. The use of a cellular confinement system will be employed to create the drive that encroaches into the RPA of T8 without having adverse effects.
- 3.6.2. A cellular confinement system provides a load transfer mattress which prevents direct loads on tree roots and reduces the bearing pressure on subsoil's by stabilising aggregate surfaces against rutting under wheel loads. Figure 3 shows a side view of the cellular confinement system.


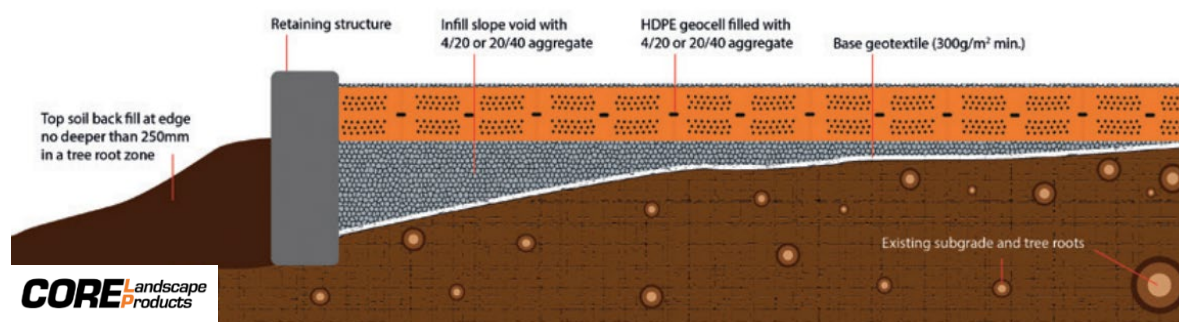


Figure 3 A side view of a cellular confinement system courtesy Core LP (for more details visit <https://www.corelp.co.uk/core-tree-root-protection/>)

- 3.6.3. Edging is not required for the stability of the cellular confinement system, but it is necessary to retain the wearing course and the filling of incomplete cells at the edge of a surface. Kerb stones set in concrete haunching's dug into the ground are typical edging for standard surfaces but this method of installation is not suitable in this instance. An appropriate edging will be selected such as peg and board edging.
- 3.6.4. I have created the following methodology which lists the sequence of operations in order, necessary to complete the hardstanding with the minimum damage to the trees proposed for retention:
- Surface layer such as grass or gravel to be scraped off for levelling purposes. This can be done either by hand or by very small machinery to a maximum depth of 50mm.
 - Spread a thin layer of 4/20 or 20/40 aggregate material over the length of the proposed hardstanding area to fill any small rut and to level area.
 - Lay base geotextile material with at least 30cm overlaps. It is recommended that the base geotextile is made of polypropylene or polyester (min. 300g/m²) with a CBR puncture resistance of 4000N.
 - Extend the cellular confinement systems over the area of the proposed hardstanding.
 - Fill the voids within the Geoweb with a 4/20 or 20/40 aggregate material working into the voids. Help settlement of the stone by a minimum of four passes of a smooth roller (max. weight of 1000kg/m width without vibration), or alternatively by several passes with a tracked excavator
 - Install peg and board edge supports or other approved edging.
 - Lay an upper layer of geotextile over the Cellular Confinement System (Not required for tarmac/asphalt surfaces). The upper geotextile is required for protecting the infill matrix; this can be of the same thickness as the base layer or slightly thinner (100–300g/m²)
 - Construct finished permeable surface as required in line with guidance illustrations below.

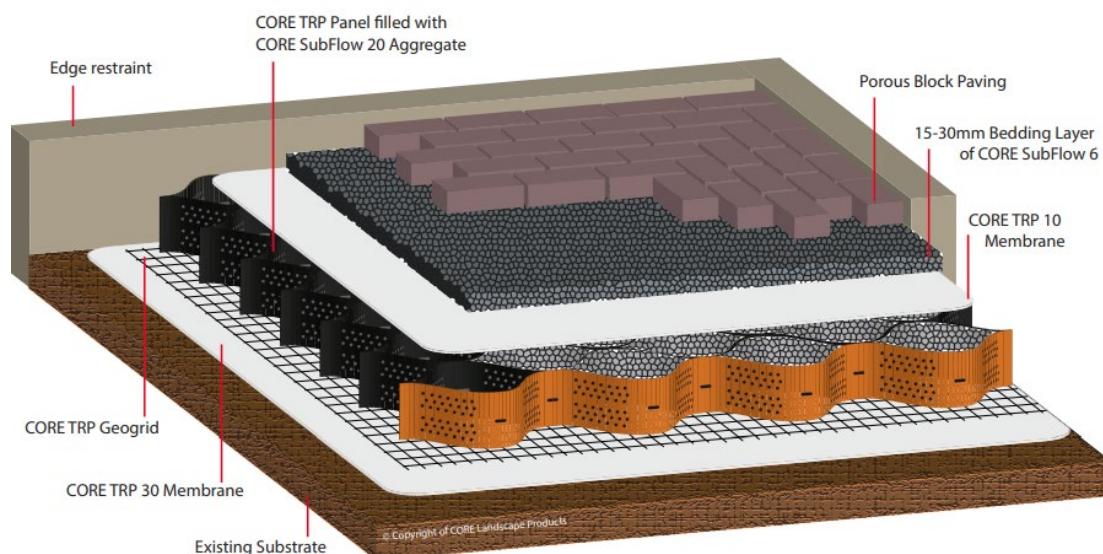

3.7. Additional Precautions Outside Fenced Areas

- 3.7.1. Oil, bitumen, cement or other material likely to cause damage to the tree will not be stacked or discharged within 10m of the trees stem or within the protective area. Also, materials in general will not be stacked or discharged within the exclusion zone.
- 3.7.2. Concrete mixing and washing will not be carried out within 10m of any retained trees.
- 3.7.3. Fires will not be lit beneath the foliage or in a position where the flames could extend to within 5m of the foliage, branches or trunk. If the fire is large, then this may necessitate a distance of at least 20m.
- 3.7.4. Trees that are to be retained will not be used as anchorage for equipment.
- 3.7.5. Notice boards, telephone cables, or other services will not be attached to any part of the retained tree.
- 3.7.6. Care should be taken when using cranes or other equipment near the canopy of the retained trees. Also, any trees to be felled in proximity to the retained trees should be done so with particular care.

3.8. Demolition adjacent to Trees & RPAs

3.8.1. During demolition, the following restrictions will apply:


- Where direct damage by falling masonry is likely, the tree should be protected by exterior grade plywood sheets constructed around the main stem.
- The main body of any mechanical excavator will operate outside the RPA.
- Masonry will be pulled away from trees.
- When breaking masonry, a fine water spray will be used to minimise dust particles if it is likely to cover leaves.
- Excessive dust particles on trees will be removed each day by spraying with water.
- Hard surfaces should be kept in place for as long as possible during construction works in order to prevent soil compaction in the RPA.

3.9. Site Monitoring

- 3.9.1. An auditable system of site monitoring shall be established to guide contractors on site, ensure that tree protection measures are implemented and adhered to, and also to demonstrate to the LPA that any planning conditions have been met.
- 3.9.2. This includes site visits by an arboricultural consultant (as appointed by the developer) to confirm the correct installation of the protective fencing, to oversee sensitive elements of works within the RPA of retained trees and sign off the site when the works are complete before fencing can be removed.
- 3.9.3. A site visit schedule has been made available in appendix II.

Appendix I

Tree Removal Plan & Tree Protection Plan



Do not scale this drawing (printed or electronic version).
Contractors must check all dimensions from site
This drawing is for use on this site only and should be used in conjunction with all relevant consultants drawings..


LEGEND



- Retained Trees
- Removed Trees
- Section of Crown Removed
- Root Protection Areas
- Position estimated on site



Scale:	1:200 @ A3	Date:	18/12/2025
Job:	2524_AIA.01		
Address	Cemetery Rd, Ramsbottom, Bury, BL0 9PU		
Client:	Home Park Avenue Ltd		
Drawing Number:	2524_TRP.02		
Drawn by:	Matthew Lally		
TREE REMOVAL PLAN			

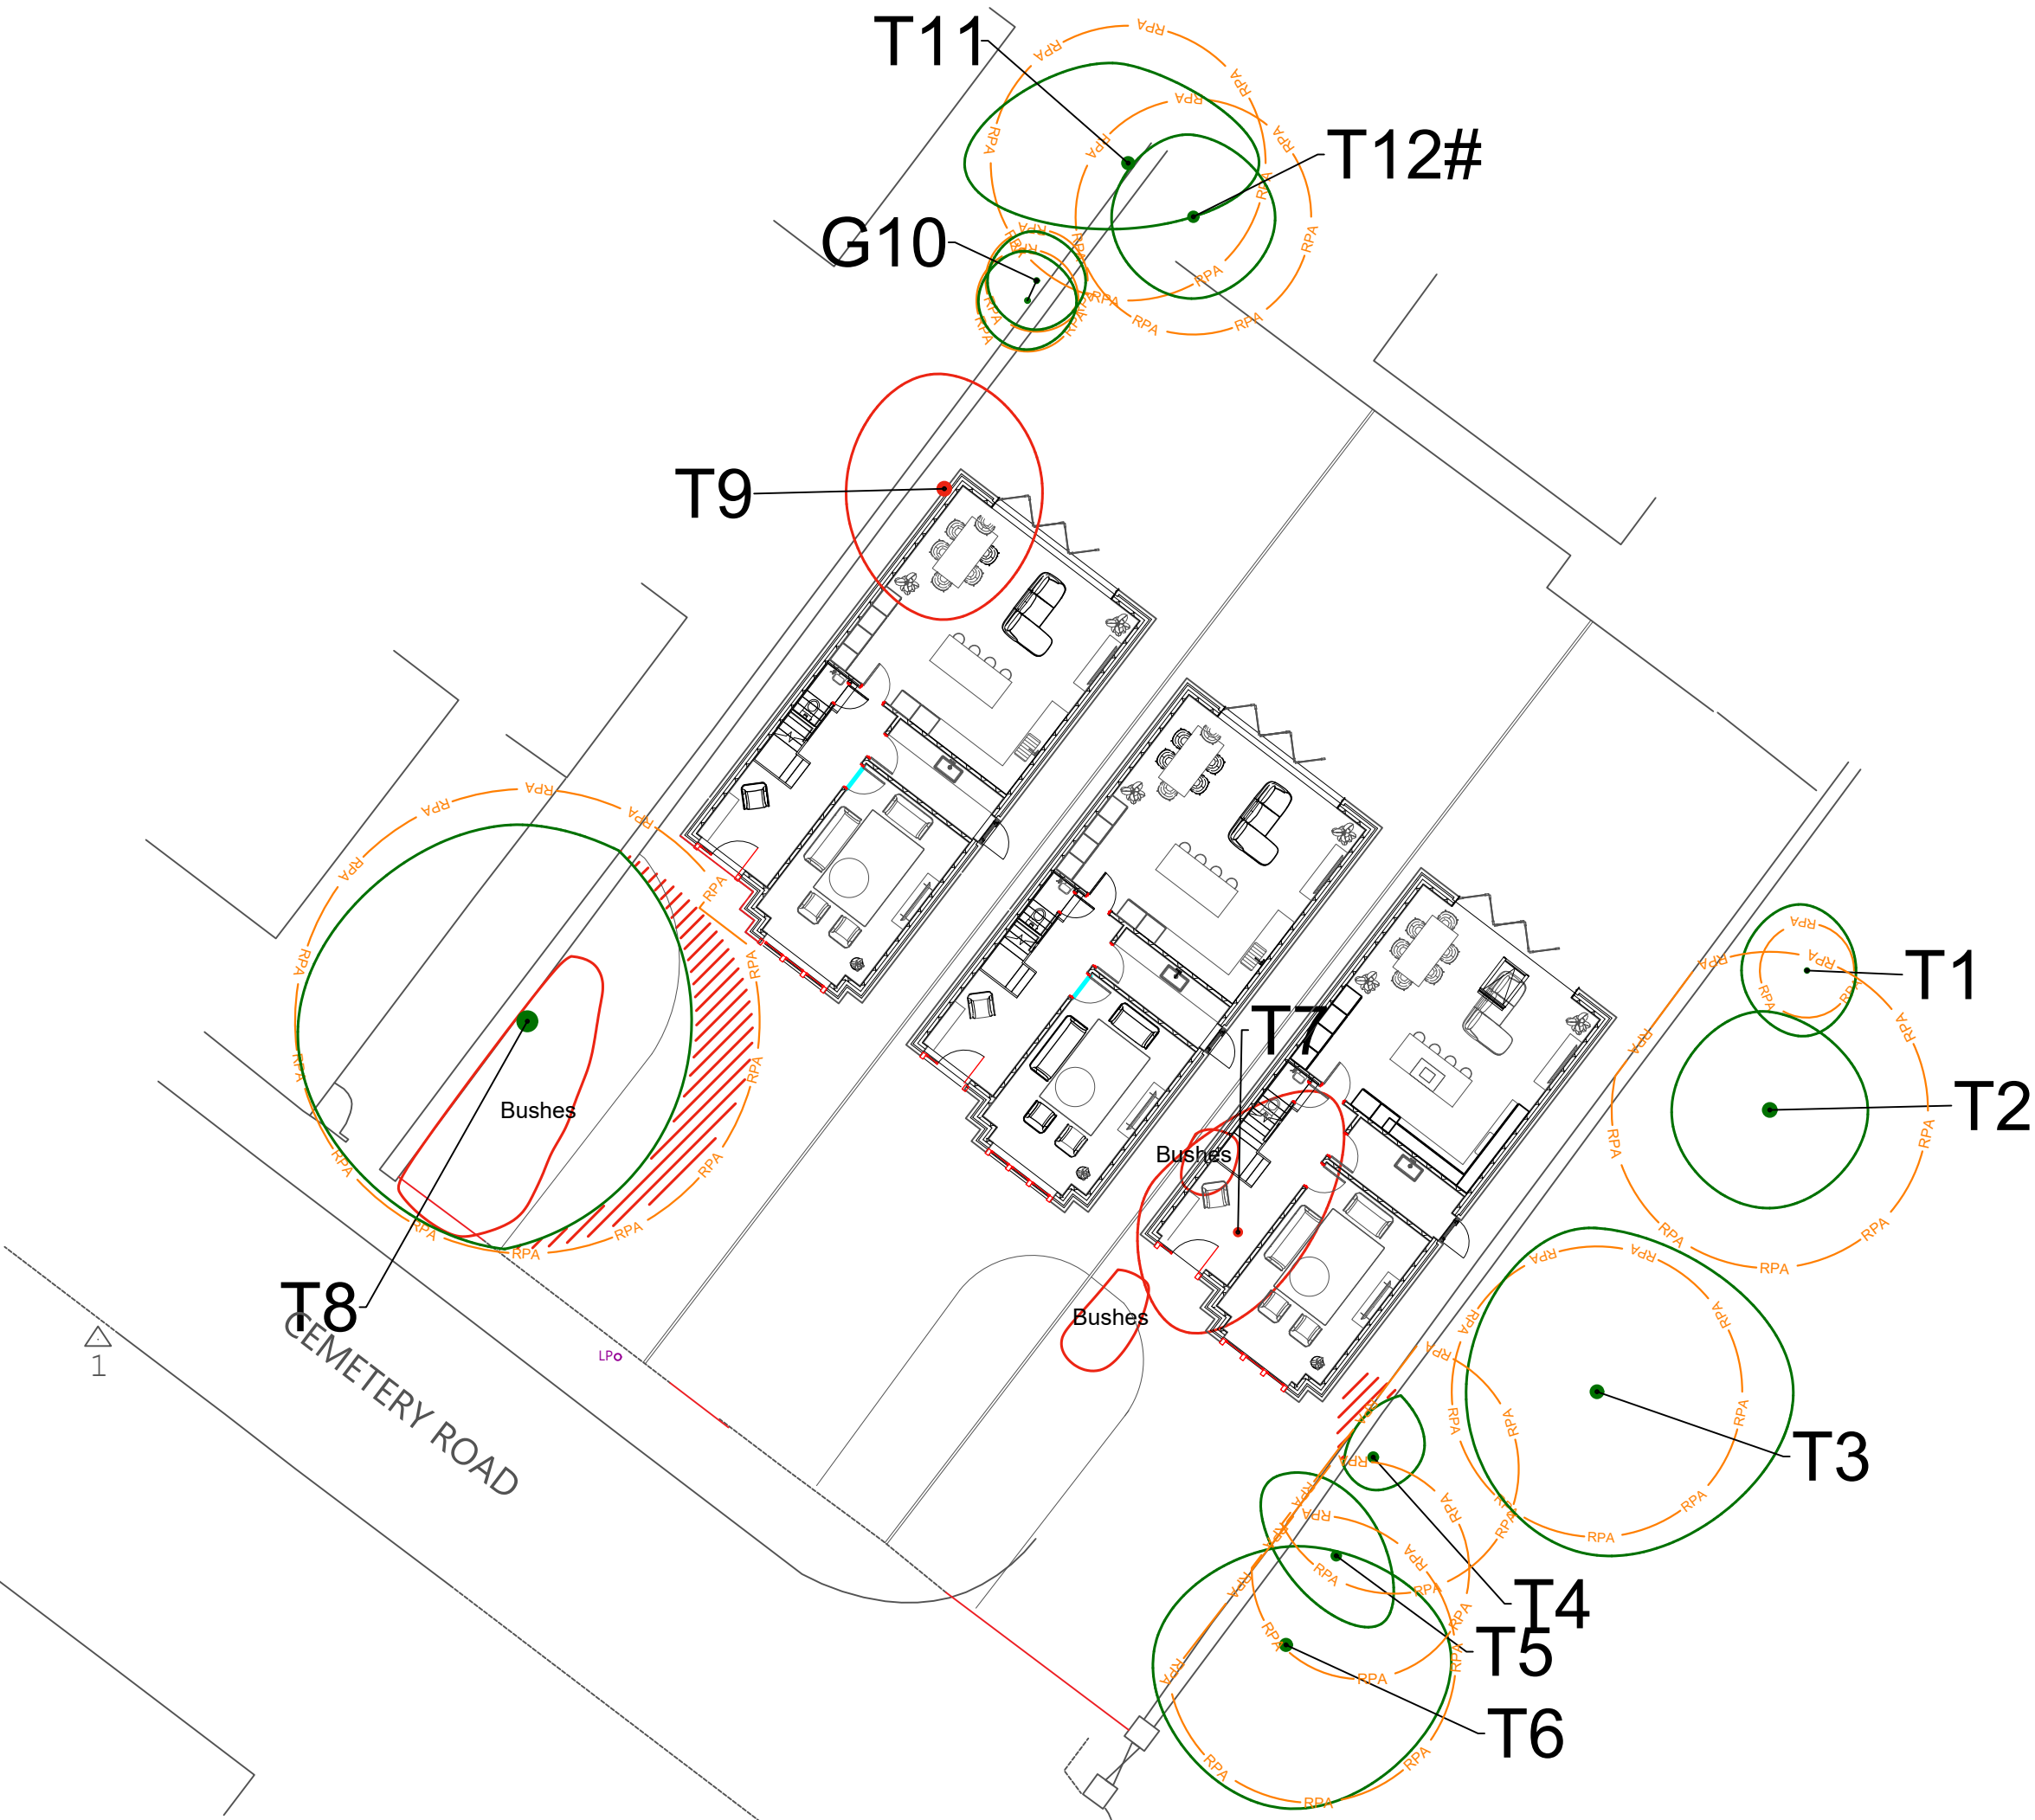

Do not scale this drawing (printed or electronic version).
Contractors must check all dimensions from site
This drawing is for use on this site only and should be used in conjunction with all relevant consultants drawings..

LEGEND





- Retained Trees
- Root Protection Areas
- Protective Fencing (Metal)
- Cellular Confinement System

Position estimated on site



Scale:	1:200 @ A3	Date:	18/12/2025
Job:	2524_AIA.01		
Address	Cemetery Rd, Ramsbottom, Bury, BL0 9PU		
Client:	Home Park Avenue Ltd		
Drawing Number:	2524_TPP.02		
Drawn by:	Matthew Lally		
TREE PROTECTION PLAN			

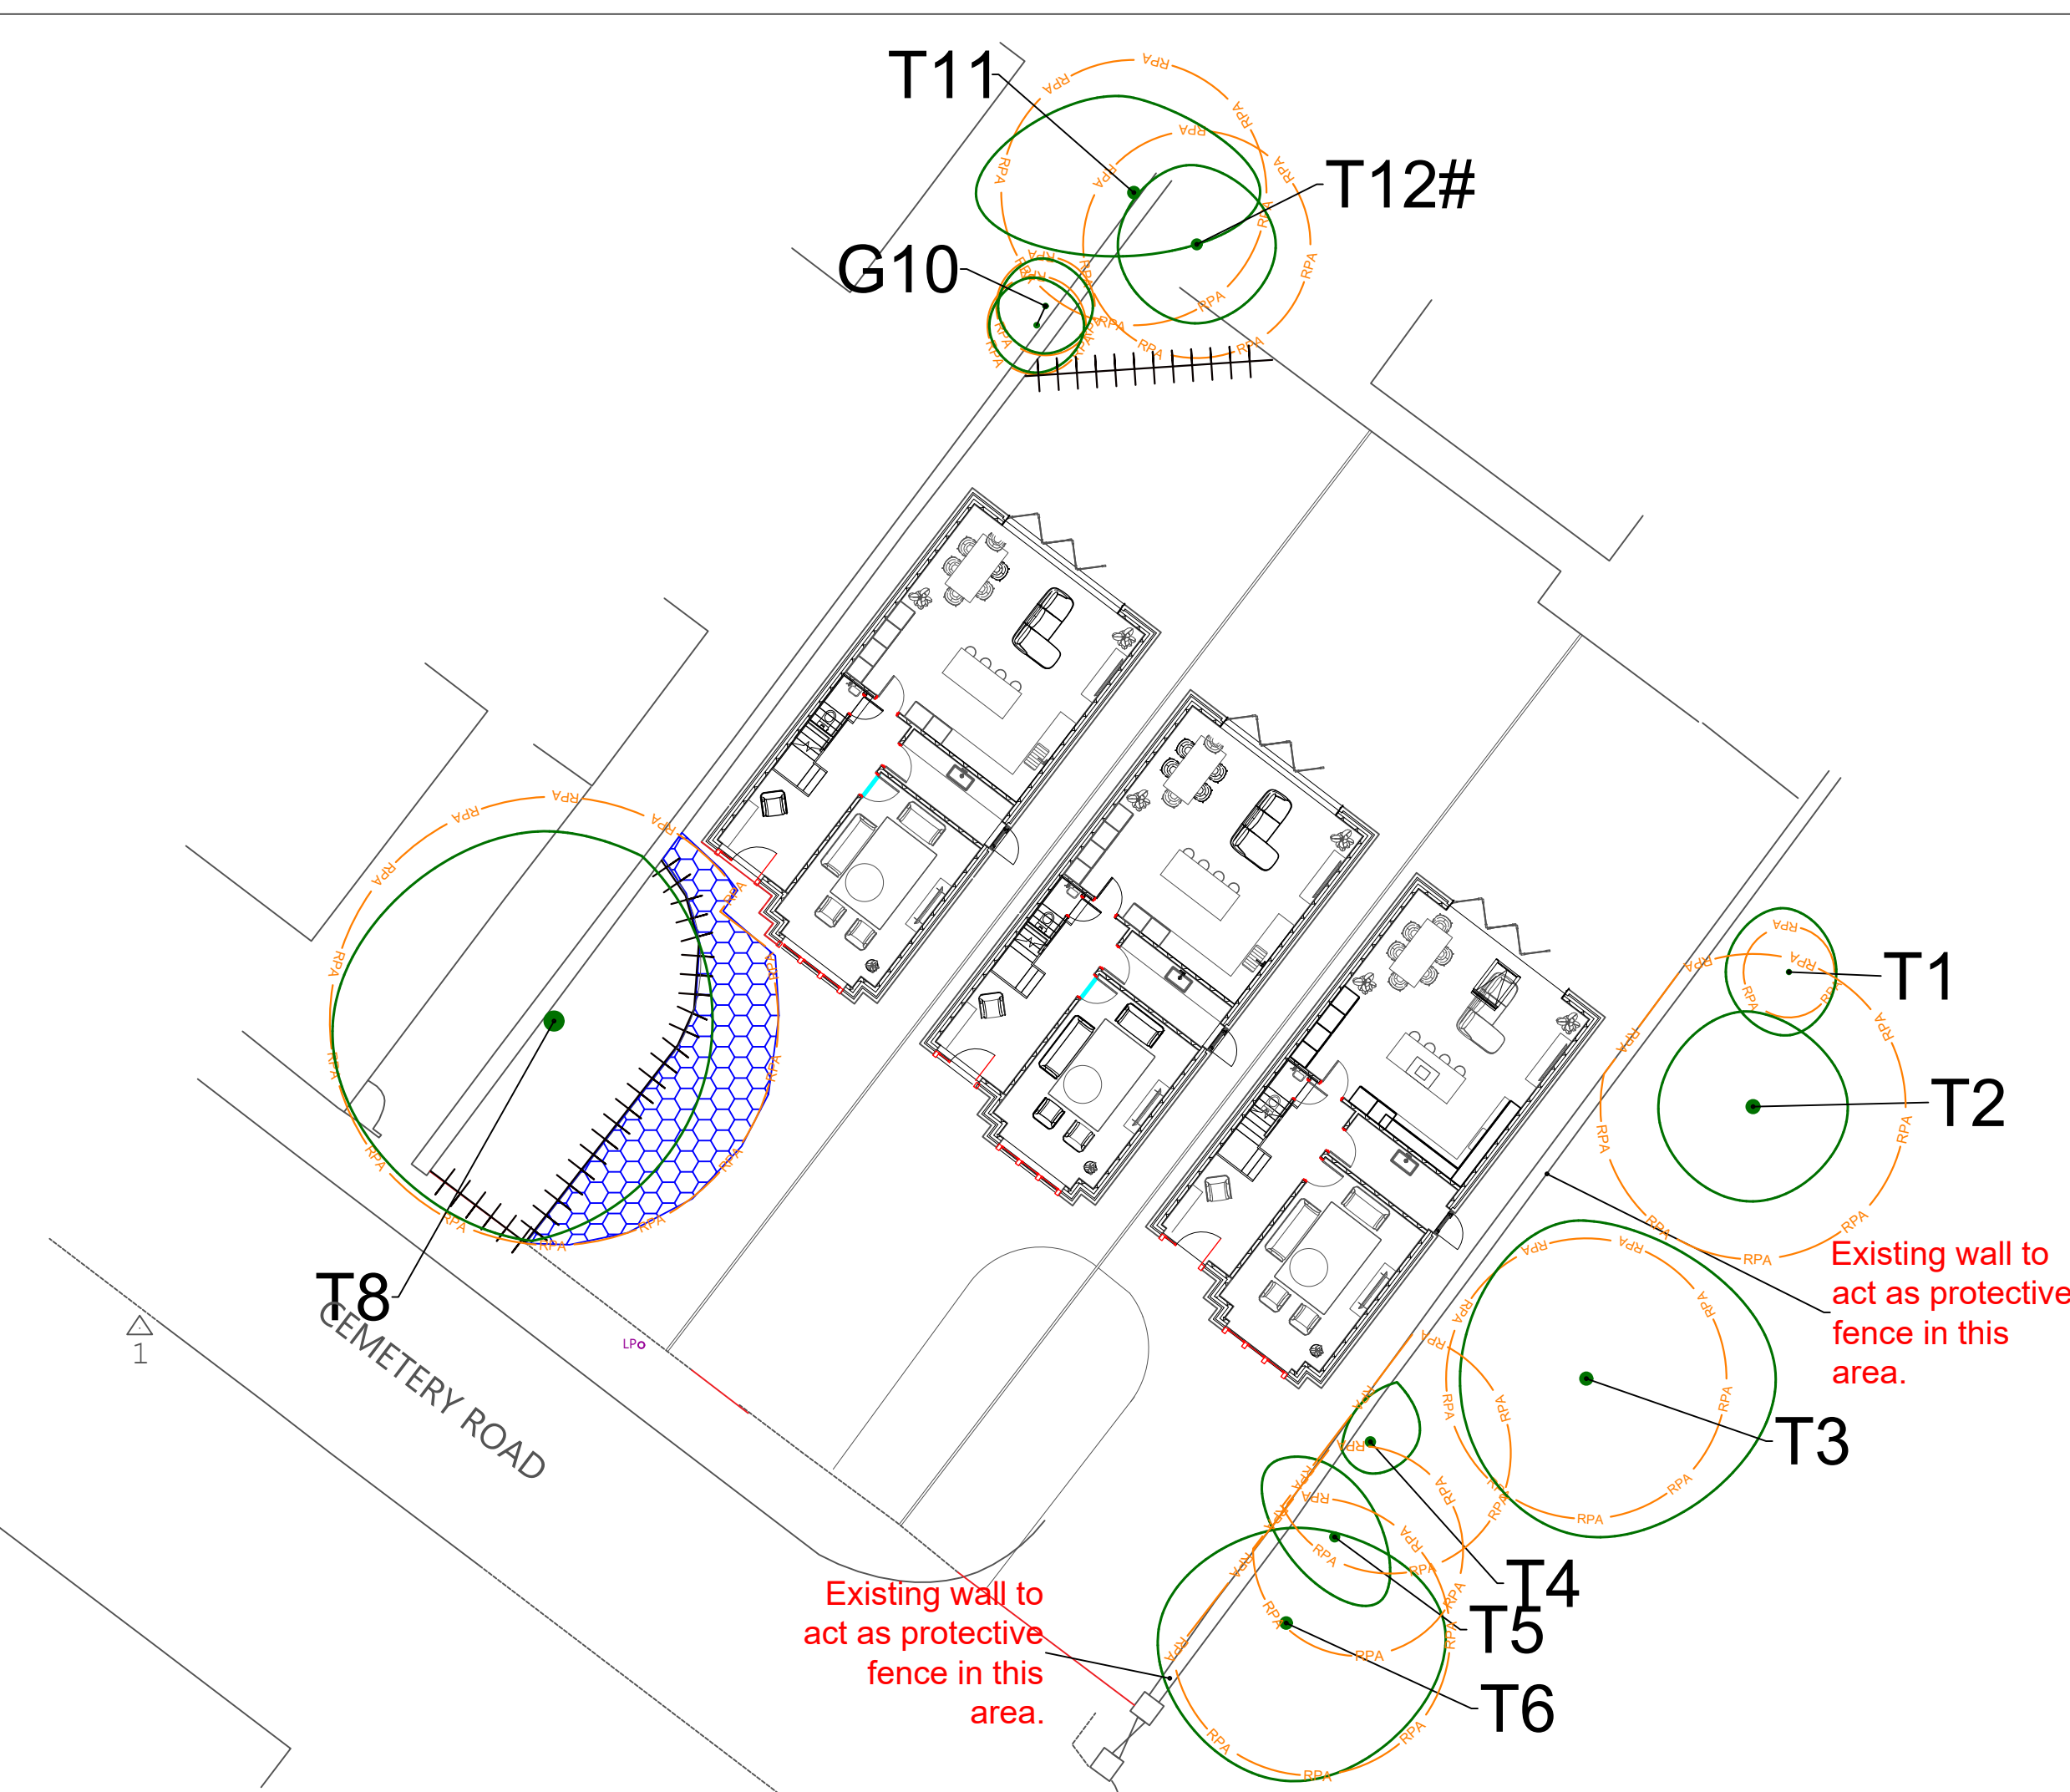



Appendix II

Auditable Site Monitoring

Tree Number	Task	Date Completed	Signed (Project Arboriculturist)	Notes	Signed (Site Manager)
Site	Pre-commencement site meeting				
See section 3.3	Tree pruning & removal sign off				
Site	Installation of protective fencing sign off				
T8	Installation of cellular confinement system sign off				
Completion of Construction					
Site	Removal of protective fencing and sign off from Project Arboriculturist				
