

Our Ref: 233579-01/PH/jt
Date: 3rd September 2025

For the attention of Francesca Monks

Kier Construction North & Scotland
3rd Floor Optimum House
Clippers Quay
Salford
M50 3XP

Re: Millwood School, Bury - As Built Information for the Health & Safety File

Dear Francesca

Please find enclosed 1 copy of the As Built Information for the Health & Safety File relating to the above contract for your records, this includes as built drawings, daily logs and test results Plt01-Plt06 and Df01-Df02.

With regards to the works carried out within this phase, good compaction pressures and stone consumption has been recorded along with acceptable validation testing results, therefore we are satisfied that the bearing pressure of 100kN/m² beneath main foundations and 25kN/m² beneath slab, has been achieved.

Should you require any further information please do not hesitate to contact the undersigned.

Yours faithfully,



Phil Hall
Operations Manager

Site Investigation
Drilling & Grouting
Ground Anchors & Soil Nails
Piling
Restricted Access Piling
Smartfoot® Precast Concrete Foundations
Ground Improvement



The Genesis Centre
Garrett Field
Birchwood
Warrington
WA3 7BH

info@van-elle.co.uk www.van-elle.co.uk

WORKING PLATFORM LEVEL=mOD


NOTES:

1. ALL DIMENSION ARE IN mm UNLESS STATED OTHERWISE.
2. REQUIREMENTS AFTER VIBRO GROUND IMPROVEMENT:

• THE NATURE OF VIBRO IS SUCH THAT THE UPPER 500mm OF TREATED GROUND CANNOT BE GUARANTEED. THIS IS DUE TO THE LACK OF LATERAL RESTRAINT CLOSE TO THE SURFACE. WE REQUIRE THAT THE TOP 500mm IS EXCAVATED / RE-COMPACTED BY OTHERS AT NO COST TO OURSELVES.

• LEVELLING OFF AND PROOF ROLLING OF THE SUB-GRADE BY THE MAIN CONTRACTOR / GROUND-WORKER FOLLOWING COMPLETION OF VIBRO GROUND IMPROVEMENT BY THE SPECIALIST GROUND IMPROVEMENT CONTRACTOR IS NORMALLY ACCEPTABLE PRIOR TO CONSTRUCTION OF GROUND BEARING FLOOR SLABS, UNLESS ADVISED OTHERWISE DUE TO PROJECT SPECIFIC REQUIREMENTS.
3. THIS DRAWING IS BASED ON THE FOLLOWING DRAWINGS RECEIVED FROM BRADSHAW GASS & HOPE LLP:

• MSE-BGH-02-00-DR-S-1001

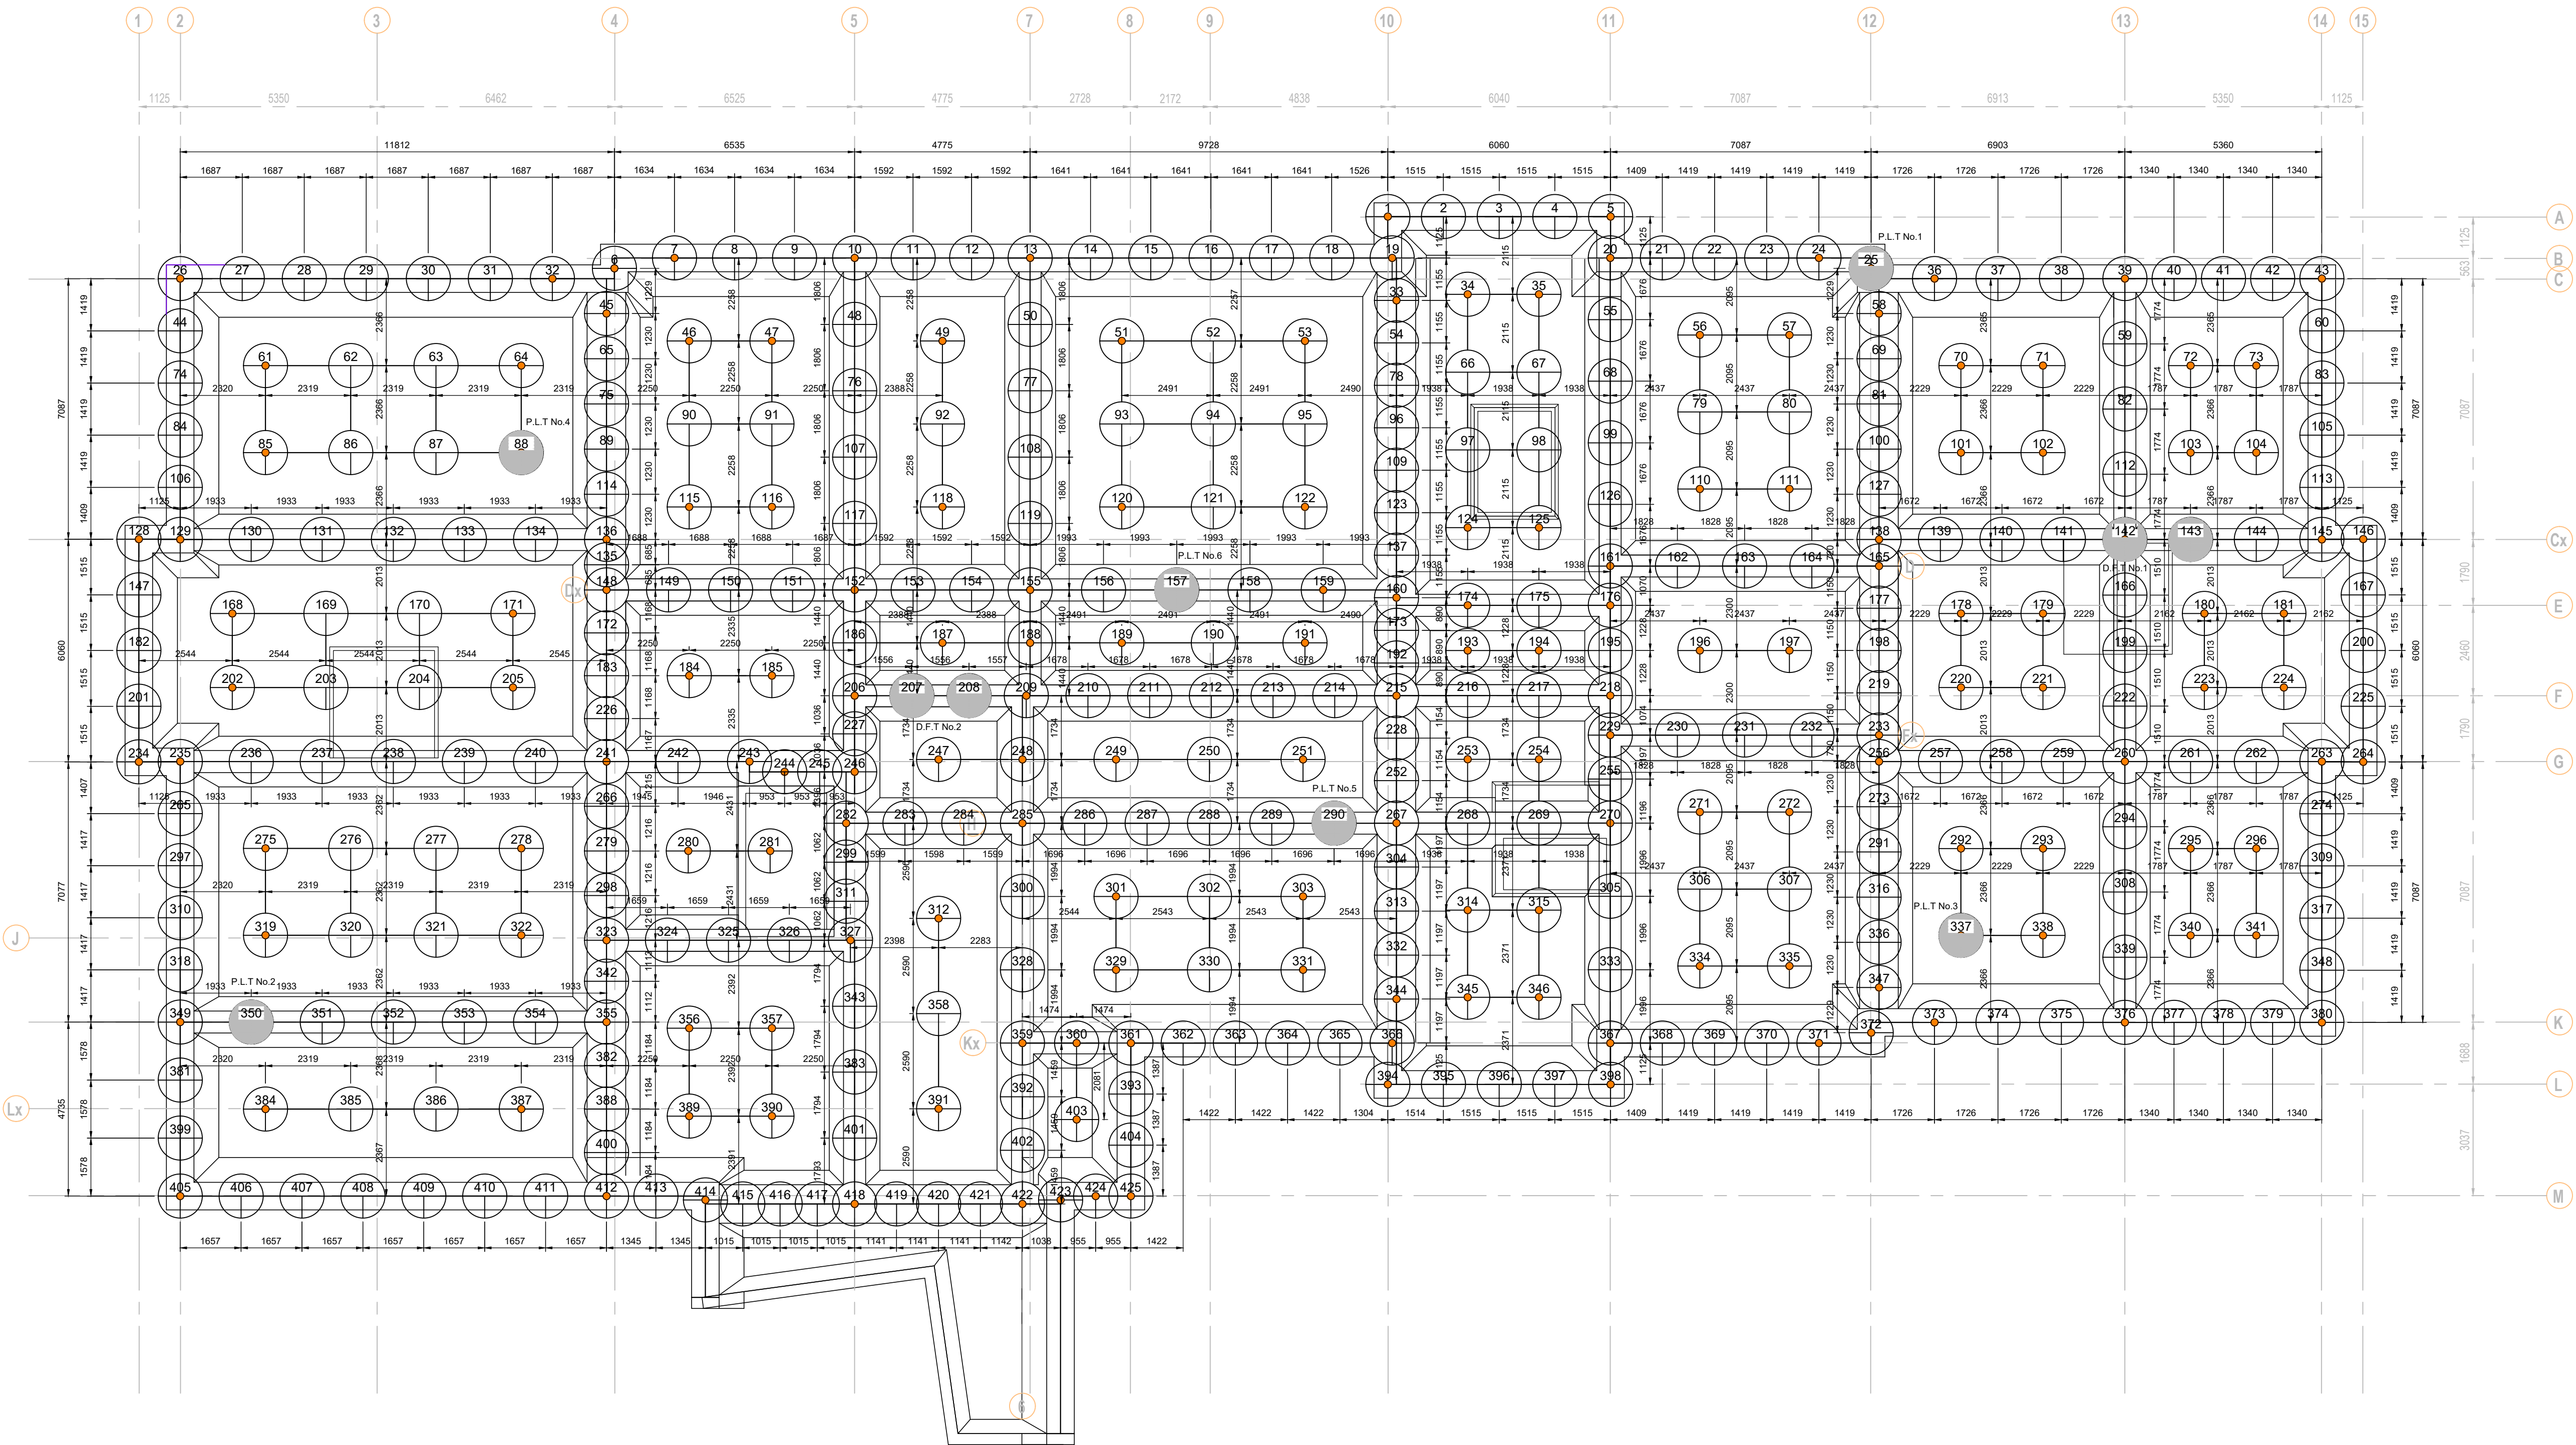

STONE COLUMNS SIZE IS NOT TO SCALE

COLUMN INSTALLATION DATE:

AB01	28.08.25	AS BUILT	L.B	
CO1	19.08.25	CONSTRUCTION ISSUE	L.B	S.A
PO1	24.07.25	FIRST ISSUE	L.B	S.A
REV	DATE	DESCRIPTION	BY	CHECK

BEARING PRESSURES kN/m²		No. of POINTS
MAIN FOUNDATIONS	SLAB	
100	25	425

SETTING OUT POINTS. INDICATES COLUMNS TO BE SET OUT ON SITE BY MAIN CONTRACTOR. ALL DIMENSIONS FOR SETTING OUT ARE TO BE TAKEN FROM ENGINEERS AND ARCHITECTS DRAWINGS.

DRAWING STATUS	STATUS CODE
AS BUILT	A5

CLIENT
Kier Construction

PROJECT
Millwood School, Bury

TITLE
Vibro Layout

VAN ELLE

TOTAL FOUNDATION SOLUTIONS

The Genesis Centre, Garrett Field, Birchwood, Warrington, WA3 7BH

01925 394968 | www.van-elle.co.uk

DRAWN	DATE	SCALE
L.B	24.07.25	1:100 @ A1
CHECKED	DATE	PROJECT CODE
S.A	24.07.25	233579-01

DRAWING NUMBER	REV
MSE-VAN-XX-XX-DR-X-0001	AB01

Vibro Stone Column Daily Log



CONTRACT: BURM JOB NO: 233 S79 -01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS FRIDAY
RIG: VB027 SHOVEL: ST199 SHEET: 1 DATE: 15/8/25

Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments	
				Boring	Packing	Boring	Packing	(Plot/Obstructions/Stoppages)	
1	110	S.S	1-S						
2	111								
3	39								
4	40								
5	41								
6	42								
7	43								
8	60								
9	73								
10	83								
11	105								
12	104								
13	113								
14	145								
15	146								
16	167								
17	200								
18	144								
19	181								
20	143								
21	180								
22	142								
23	166								
24	199								
25	179	S.S	1-S						
TOTAL	25	137.5	37.5	PLATE TEST				TO DATE	
PREVIOUS	48	264	72	DUMMY TEST				TO DATE	
TO DATE	73	401.5	109.5	WEATHER CONDITIONS					

I CONFIRM THIS IS A TRUE RECORD.

VE NAME A. KENNEDY CLIENT'S NAME J. RIVERS

VE POSITION S.S CLIENT'S POSITION S.M

SIGNED [Signature] SIGNED [Signature]

DATED 15/8/25 DATED 18/8/25

CONTRACT: Bury JOB NO: 233579 - 01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS								
RIG: <u>VB07</u>		SHOVEL: <u>ST199</u>		SHEET: <u>2</u>		DATE: <u>15/8/23</u>		
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	10	S.S	1-S					
2	76							
3	9							
4	47							
5	91							
6	8							
7	7							
8	46							
9	90							
10	6							
11	45							
12	65							
13	75							
14	64							
15	88							
16	63							
17	87							
18	62							
19	86							
20	61							
21	85							
22	11							
23	48							
24	32							
25	31	S.S	1-S					
TOTAL	25	137.5	37.5			PLATE TEST		TO DATE
PREVIOUS	73	401.5	109.5			DUMMY TEST		TO DATE
TO DATE	98	539	147			WEATHER CONDITIONS		

I CONFIRM THIS IS A TRUE RECORD. VE NAME <u>A. KENNEDY</u> VE POSITION <u>S.S</u> SIGNED <u>A Kennedy</u> DATED <u>15/8/23</u>	CLIENT'S NAME <u>J. RUTS</u> CLIENT'S POSITION <u>S.M</u> SIGNED <u>JR</u> DATED <u>18/8/23</u>
--	--

CONTRACT: BULLY JOB NO: 233579-01
DAILY RECORD LOG FOR VIBRO STONE COLUMNS
RIG: V5127 SHOVEL: ST199 SHEET: 3 DATE: 15/8/25 FRI DAY

Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments	
				Boring	Packing	Boring	Packing	(Plot/Obstructions/Stoppages)	
1	30	5.5	1.5						
2	29								
3	28								
4	27								
5	26								
6	44								
7	74								
8	84								
9	106								
10	128								
11	129								
12	130								
13	147								
14	182								
15	201								
16	234								
17	235								
18	265								
19	297								
20	310								
21	318								
22	349								
23	350								
24	381								
25	399			5.5	1.5				
TOTAL	25	137.5	37.5			PLATE TEST		TO DATE	
PREVIOUS	98	539	147			DUMMY TEST		TO DATE	
TO DATE	123	676.5	184.5			WEATHER CONDITIONS			

I CONFIRM THIS IS A TRUE RECORD.

VE NAME A. KENNEDY CLIENT'S NAME J. RIVERS

VE POSITION PS CLIENT'S POSITION SM

SIGNED [Signature] SIGNED [Signature]

DATED 15/8/25 DATED 18/8/25

CONTRACT: Bury JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS FLIDAY

RIG:		SHOVEL:		SHEET: <u>4</u>		DATE: <u>15/8/25</u>		
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	405	S.S	1.5					
2	406	S.S	1.5					
3	407	S.S	1.5					
4	408	S.S	1.5					
5								
6								
7								
8								
9								
10								
11								
12								
13								
14								
15								
16								
17								
18								
19								
20								
21								
22								
23								
24								
25								
TOTAL	<u>4</u>	<u>22</u>	<u>6</u>			PLATE TEST		TO DATE
PREVIOUS	<u>123</u>	<u>676.5</u>	<u>184.5</u>			DUMMY TEST		TO DATE
TO DATE	<u>127</u>	<u>698.5</u>	<u>190.5</u>			WEATHER CONDITIONS		

I CONFIRM THIS IS A TRUE RECORD.			
VE NAME <u>A. KENNEDY</u>	CLIENT'S NAME <u>J. C. WILSON</u>		
VE POSITION <u>S.S</u>	CLIENT'S POSITION <u>S.M</u>		
SIGNED <u>[Signature]</u>	SIGNED <u>[Signature]</u>		
DATED <u>15/8/25</u>	DATED <u>15/8/25</u>		

CONTRACT: BURY JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS								
RIG: <u>VB27</u>		SHOVEL: <u>ST 199</u>		SHEET: <u>1</u>		DATE: <u>14/8/25</u>		
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	38	S.S	1.5					MILLWOOD
2	71							SCHOOL
3	70							
4	37							
5	36							
6	58							
7	25							
8	24							
9	23							
10	22							
11	21							
12	20							
13	5							
14	4							
15	3							
16	2							
17	1							
18	19							
19	18							
20	17							
21	16							
22	15							
23	14							
24	13							
25	12	S.S	1.5					
TOTAL	25	137.5	37.5			PLATE TEST		TO DATE
PREVIOUS						DUMMY TEST		TO DATE
TO DATE	25	137.5	37.5			WEATHER CONDITIONS		

I CONFIRM THIS IS A TRUE RECORD.			
VE NAME	<u>AUGUSTIN</u>	CLIENT'S NAME	<u>J. RIVERS</u>
VE POSITION	<u>S.S</u>	CLIENT'S POSITION	<u>S.M</u>
SIGNED	<u>[Signature]</u>	SIGNED	<u>[Signature]</u>
DATED	<u>14/8/25</u>	DATED	<u>15/8/25</u>

CONTRACT: <u>BUR4</u>	JOB NO: <u>233579-01</u>
-----------------------	--------------------------

DAILY RECORD LOG FOR VIBRO STONE COLUMNS								
RIG: <u>V827</u>		SHOVEL: <u>ST199</u>		SHEET: <u>2</u>		DATE: <u>THURS 14/8/25</u>		
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	72	S.S	1-S					
2	103							
3	59							
4	82							
5	112							
6	102							
7	101							
8	69							
9	81							
10	100							
11	80							
12	57							
13	56							
14	79							
15	55							
16	68							
17	99							
18	35							
19	67							
20	98							
21	34							
22	66							
23	97	S.S	1-S					
24								
25								
TOTAL	23	126.5	34.5			PLATE TEST		TO DATE
PREVIOUS	25	137.5	37.5			DUMMY TEST		TO DATE
TO DATE	48	264	72			WEATHER CONDITIONS		

I CONFIRM THIS IS A TRUE RECORD. VE NAME <u>A. KENNEDY</u> VE POSITION <u>S.S</u> SIGNED <u>[Signature]</u> DATED <u>14/8/25</u>	CLIENT'S NAME <u>J. RIVERS</u> CLIENT'S POSITION <u>S.M</u> SIGNED <u>[Signature]</u> DATED <u>15/8/25</u>
---	--

Vibro Stone Column Daily Log



CONTRACT: BUEY JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS

RIG: VB27 SHOVEL: ST199 SHEET: 1 DATE: THURS 21/8/25

Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments	
				Boring	Packing	Boring	Packing	(Plot/Obstructions/Stoppages)	
1	355	S.S	1.5						
2	382								
3	388								
4	400								
5	412								
6	133								
7	134								
8	170								
9	171								
10	204								
11	205								
12	238								
13	239								
14	240								
15	277								
16	278								
17	321								
18	322								
19	353								
20	354								
21	386								
22	387								
23	409								
24	410								
25	411	S.S	1.5						
TOTAL	25	137.5	37.5			PLATE TEST		TO DATE	
PREVIOUS	350	1937.5	525			DUMMY TEST		TO DATE	
TO DATE	375	2075	662.5			WEATHER CONDITIONS			

I CONFIRM THIS IS A TRUE RECORD.

VE NAME B. McElwain

VE POSITION S/S

SIGNED [Signature]

DATED 21/8/25

CLIENT'S NAME

CLIENT'S POSITION

SIGNED [Signature]

DATED 21/08/25

Vibro Stone Column Daily Log



CONTRACT: BURY JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS								
RIG: <u>VR07</u>		SHOVEL: <u>ST199</u>		SHEET: <u>2</u>		DATE: <u>THURS 21/8/25</u>		
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	107	S.S	1.S					
2	117							
3	152							
4	186							
5	206							
6	227							
7	246							
8	282							
9	299							
10	311							
11	327							
12	343							
13	383							
14	115							
15	116							
16	149							
17	150							
18	151							
19	184							
20	185							
21	242							
22	243							
23	244							
24	245							
25	281	S.S	1.S					
TOTAL	25	137.5	37.5			PLATE TEST		TO DATE
PREVIOUS	375	207.5	562.5			DUMMY TEST		TO DATE
TO DATE	400	222.5	600			WEATHER CONDITIONS		

I CONFIRM THIS IS A TRUE RECORD.

VE NAME

VE POSITION.....

SIGNED.....

DATED

CLIENT'S NAME

CLIENT'S POSITION

SIGNED

DATED 21/8/25

CONTRACT: BUR4 JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS THURS

RIG: UB07 SHOVEL: ST199 SHEET: 3 DATE: 21/8/25

Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	280	S.S	1-S					
2	324							
3	325							
4	326							
5	356							
6	357							
7	389							
8	390							
9	413							
10	414							
11	415							
12	416							
13	417							
14	136							
15	135							
16	148							
17	172							
18	183							
19	226							
20	241							
21	266							
22	279							
23	298							
24	323							
25	342	S.S	1-S					
TOTAL	25	137.5	37.5	PLATE TEST		TO DATE		
PREVIOUS	400	2212.5	600	DUMMY TEST		TO DATE		
TO DATE	425	2350	637.5	WEATHER CONDITIONS				

I CONFIRM THIS IS A TRUE RECORD.

VE NAME
VE POSITION.....
SIGNED.....
DATED

CLIENT'S NAME J. Edwards
CLIENT'S POSITION Site manager
SIGNED [Signature]
DATED 21/08/25

Vibro Stone Column Daily Log



CONTRACT: BWM JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS

RIG: V307 SHOVEL: ST199 SHEET: 1 DATE: 20/8/25

Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)	
				Boring	Packing	Boring	Packing		
1	52	5.5	1.5						
2	53								
3	94								
4	95								
5	121								
6	122								
7	157								
8	158								
9	159								
10	190								
11	191								
12	212								
13	213								
14	214								
15	250								
16	251								
17	289								
18	288								
19	302								
20	303								
21	425								
22	424								
23	423								
24	404								
25	403			5.5	1.5				
TOTAL	25	137.5	37.5	PLATE TEST				TO DATE	
PREVIOUS	275	152.5	412.5	DUMMY TEST				TO DATE	
TO DATE	300	166.5	450	WEATHER CONDITIONS					

I CONFIRM THIS IS A TRUE RECORD.

VE NAME A. LEONARDY

VE POSITION S.S.

SIGNED A. Leonardy

DATED 20/8/25

CLIENT'S NAME

CLIENT'S POSITION

SIGNED [Signature]

DATED 20/8/25

CONTRACT: BULY JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS								
RIG: <u>VIB27</u>		SHOVEL: <u>ST199</u>		SHEET: <u>2</u>		DATE: <u>WED 20/8/25</u>		
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	422	5.5	1.5					
2	402							
3	392							
4	393							
5	359							
6	360							
7	361							
8	362							
9	329							
10	328							
11	300							
12	301							
13	285							
14	286							
15	287							
16	248							
17	249							
18	209							
19	210							
20	211							
21	188							
22	189							
23	155							
24	156							
25	119	5.5	1.5					
TOTAL	25	137.5	37.5			PLATE TEST		TO DATE
PREVIOUS	300	1662.5	450			DUMMY TEST		TO DATE
TO DATE	325	1800	487.5			WEATHER CONDITIONS		
I CONFIRM THIS IS A TRUE RECORD. VE NAME <u>Alex Wray</u> VE POSITION <u>S.S</u> SIGNED <u>Alex Wray</u> DATED <u>20/8/25</u>				CLIENT'S NAME CLIENT'S POSITION SIGNED <u>[Signature]</u> DATED <u>20/8/25</u>				

Vibro Stone Column Daily Log



CONTRACT: BURY JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS

RIG: <u>VB27</u>		SHOVEL: <u>ST99</u>		SHEET: <u>3</u>		DATE: <u>20/8/25</u>		
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	51	5.5	1-S					
2	93							
3	120							
4	50							
5	49							
6	77							
7	92							
8	108							
9	118							
10	153							
11	154							
12	187							
13	207							
14	208							
15	247							
16	283							
17	284							
18	312							
19	358							
20	391							
21	401							
22	418							
23	419							
24	420							
25	421	5.5	1-S					
TOTAL	25	137.5	37.5			PLATE TEST		TO DATE
PREVIOUS	325	1800	487.5			DUMMY TEST		TO DATE
TO DATE	350	1937.5	525			WEATHER CONDITIONS		

I CONFIRM THIS IS A TRUE RECORD. VE NAME <u>A. Kennedy</u> VE POSITION <u>S.S.</u> SIGNED <u>A. Kennedy</u> DATED <u>20/8/25</u>		CLIENT'S NAME <u>J. Edwards</u> CLIENT'S POSITION <u>Site manager</u> SIGNED <u>J. Edwards</u> DATED <u>20/08/25</u>	
--	--	---	--

Vibro Stone Column Daily Log



CONTRACT: BURY JOB NO: 233S79-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS

RIG: <u>VR27</u>		SHOVEL: <u>ST199</u>		SHEET: <u>1</u>		DATE: <u>19/8/25</u>		
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	96	S.S	1-S					
2	109							
3	123							
4	124							
5	125							
6	126							
7	137							
8	161							
9	162							
10	163							
11	160							
12	174							
13	175							
14	176							
15	173							
16	193							
17	194							
18	195							
19	196							
20	215							
21	216							
22	217							
23	218							
24	228							
25	253	S.S	1-S					
TOTAL	25	137.5	37.5	PLATE TEST		TO DATE		
PREVIOUS	213	1184	319.5	DUMMY TEST		TO DATE		
TO DATE	238	1321.5	357	WEATHER CONDITIONS				

I CONFIRM THIS IS A TRUE RECORD.

VE NAME A. KENNEDY

VE POSITION S.S

SIGNED A. Kennedy

DATED 19/8/25

CLIENT'S NAME J. RIVERS

CLIENT'S POSITION S.M

SIGNED J. Rivers

DATED 20/8/25

CONTRACT: BW27 JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS

RIG: VB27 SHOVEL: ST199 SHEET: 2 DATE: 19/8/25 TUES

Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)		
				Boring	Packing	Boring	Packing			
1	192	S-S	1-S							
2	254									
3	284									334
4	229									
5	230									
6	231									
7	255									
8	252									
9	290									
10	267									
11	268									
12	269									
13	270									
14	271									
15	304									
16	313									
17	214									
18	215									
19	305									
20	306									
21	332									
22	344									
23	345									
24	346									
25	333			S.S	1.S					
TOTAL	25	137.5	37.5		PLATE TEST			TO DATE		
PREVIOUS	238	132.5	35.7		DUMMY TEST			TO DATE		
TO DATE	263	145.9	39.5		WEATHER CONDITIONS					

I CONFIRM THIS IS A TRUE RECORD.

VE NAME A. KENNEDY

VE POSITION S.S.

SIGNED A. Kennedy

DATED 19/8/25

CLIENT'S NAME J. RIVALS

CLIENT'S POSITION S.M.

SIGNED [Signature]

DATED 20/8/25

Vibro Stone Column Daily Log



CONTRACT: Bulky JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS

RIG: <u>W327</u>		SHOVEL: <u>ST49</u>		SHEET: <u>3</u>		DATE: <u>TUES 19/8/25</u>		
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	330	S.S	1.5					
2	331							
3	363							
4	364							
5	365							
6	366							
7	394							
8	395							
9	396							
10	397							
11	398							
12	367	S.S	1.5					
13								
14								
15								
16								
17								
18								
19								
20								
21								
22								
23								
24								
25								
TOTAL	12	66	18			PLATE TEST		TO DATE
PREVIOUS	263	1459	394.5			DUMMY TEST		TO DATE
TO DATE	275	1525	412.5			WEATHER CONDITIONS		

I CONFIRM THIS IS A TRUE RECORD. VE NAME <u>A. MUGUNY</u> VE POSITION <u>S.S</u> SIGNED <u>A. MUGUNY</u> DATED <u>19/8/25</u>		CLIENT'S NAME <u>J. RIVERS</u> CLIENT'S POSITION <u>SM</u> SIGNED <u>JR</u> DATED <u>20/8/25</u>	
---	--	---	--

Vibro Stone Column Daily Log



CONTRACT: Bucy JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS MONDAY
 RIG: VB27 SHOVEL: ST199 SHEET: 1 DATE: 18/8/25

Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)	
				Boring	Packing	Boring	Packing		
1	33	S.S	1-S						
2	54								
3	78								
4	89								
5	114								
6	131								
7	132								
8	168								
9	169								
10	202								
11	203								
12	236								
13	237								
14	275								
15	276								
16	319								
17	320								
18	351								
19	352								
20	384								
21	385								
22	222								
23	223								
24	224								
25	225			S.S	1-S				
TOTAL	25	137.5	37.5	PLATE TEST			TO DATE		
PREVIOUS	127	698.5	190.5	DUMMY TEST			TO DATE		
TO DATE	152	836	228	WEATHER CONDITIONS					

I CONFIRM THIS IS A TRUE RECORD.

VE NAME A. KENNEDY CLIENT'S NAME J. RIVERS
 VE POSITION S.S CLIENT'S POSITION S.M
 SIGNED A. Kennedy SIGNED J. Rivers
 DATED 18/8/25 DATED 19/8/25

CONTRACT: BUR4JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS

RIG: VB27SHOVEL: ST199SHEET: 2DATE: 18/8/25

Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)	
				Boring	Packing	Boring	Packing		
1	257	6	1.5						
2	258								
3	259								
4	260								
5	261								
6	262								
7	263								
8	264								
9	292								
10	293								
11	294								
12	295								
13	296								
14	274								
15	308								
16	309								
17	337								
18	338								
19	339								
20	340								
21	341								
22	317								
23	348								
24	374								
25	375			6	1.5				
TOTAL	25	150	37.5	PLATE TEST			TO DATE		
PREVIOUS	152	836	228	DUMMY TEST			TO DATE		
TO DATE	177	986	265.5	WEATHER CONDITIONS					

I CONFIRM THIS IS A TRUE RECORD.

VE NAME A. VENNEMVE POSITION SSSIGNED A. VennemDATED 18/8/25CLIENT'S NAME J. RiversCLIENT'S POSITION S.MSIGNED [Signature]DATED 19/8/25

Vibro Stone Column Daily Log



CONTRACT: Bum JOB NO: 233579-01

DAILY RECORD LOG FOR VIBRO STONE COLUMNS

RIG: <u>V1527</u>		SHOVEL: <u>ST199</u>		SHEET: <u>3</u>		DATE: <u>18/8/25</u>		MWD M	
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments	
				Boring	Packing	Boring	Packing	(Plot/Obstructions/Stoppages)	
1	376	S-S	1-S						
2	377								
3	378								
4	379								
5	380								
6	373								
7	336								
8	335								
9	347								
10	372								
11	371								
12	139								
13	140								
14	141								
15	178								
16	220								
17	221								
18	127								
19	138								
20	165								
21	164								
22	177								
23	198								
24	197								
25	219	S-S	1-S						
TOTAL	25	137.5	37.5			PLATE TEST		TO DATE	
PREVIOUS	177	986	265.5			DUMMY TEST		TO DATE	
TO DATE	202	1123.5	303			WEATHER CONDITIONS			

I CONFIRM THIS IS A TRUE RECORD.

VE NAME A. KENNEDY CLIENT'S NAME J. RIVERS

VE POSITION S.S. CLIENT'S POSITION S.M.

SIGNED A. Kennedy SIGNED J. Rivers

DATED 18/8/25 DATED 19/8/25

Vibro Stone Column Daily Log



CONTRACT: 8004 JOB NO: 233579-01


DAILY RECORD LOG FOR VIBRO STONE COLUMNS

RIG: <u>UB127</u>		SHOVEL: <u>ST199</u>		SHEET: <u>4</u>		DATE: <u>18/8/25</u>		
Count	Column No.	Depth (m)	Stone (T)	Time		Pressures		Comments (Plot/Obstructions/Stoppages)
				Boring	Packing	Boring	Packing	
1	233	5.5	1.5					
2	232							
3	256							
4	273							
5	272							
6	291							
7	307							
8	216							
9	370							
10	369							
11	368	5.5	1.5					
12								
13								
14								
15								
16								
17								
18								
19								
20								
21								
22								
23								
24								
25								
TOTAL	11	60.5	16.5			PLATE TEST		TO DATE
PREVIOUS	202	1123.5	303			DUMMY TEST		TO DATE
TO DATE	213	1184	319.5			WEATHER CONDITIONS		

I CONFIRM THIS IS A TRUE RECORD. VE NAME <u>A. AGUNOM</u> VE POSITION <u>S.S</u> SIGNED <u>[Signature]</u> DATED <u>18/8/25</u>		CLIENT'S NAME <u>J. R. W. S.</u> CLIENT'S POSITION <u>S.M</u> SIGNED <u>[Signature]</u> DATED <u>19/8/25</u>	
---	--	---	--


SHEET		1 of 1	CONTRACT No	233579-01
CONTRACT		Millwood School, Bury	DATE OF TEST	14.08.25
TEST FOOTING SIZE		600mm Dia	INSTALL DATE	14.08.25
COLUMN No		25	TEST DEPTH	250mm
PLOT No		W-site	TEST No	Plt01
TIME	ELAPSED TIME IN HOURS MIN	APPLIED LOAD TONNES		AVERAGE SETTLEMENT MM
16:30	00:00	0		0.00
16:31	00:01	1		0.25
16:35	00:05	1		0.29
16:36	00:06	3		0.70
16:40	00:10	3		0.76
16:41	00:11	5		1.25
16:45	00:15	5		1.32
16:46	00:16	7		2.11
16:50	00:20	7		2.19
16:51	00:21	9		3.01
16:55	00:25	9		3.07
16:56	00:26	11		3.69
17:05	00:35	11		3.77
17:10	00:40	0		1.82
17:15	00:45	0		1.71

PLATE LOAD TEST

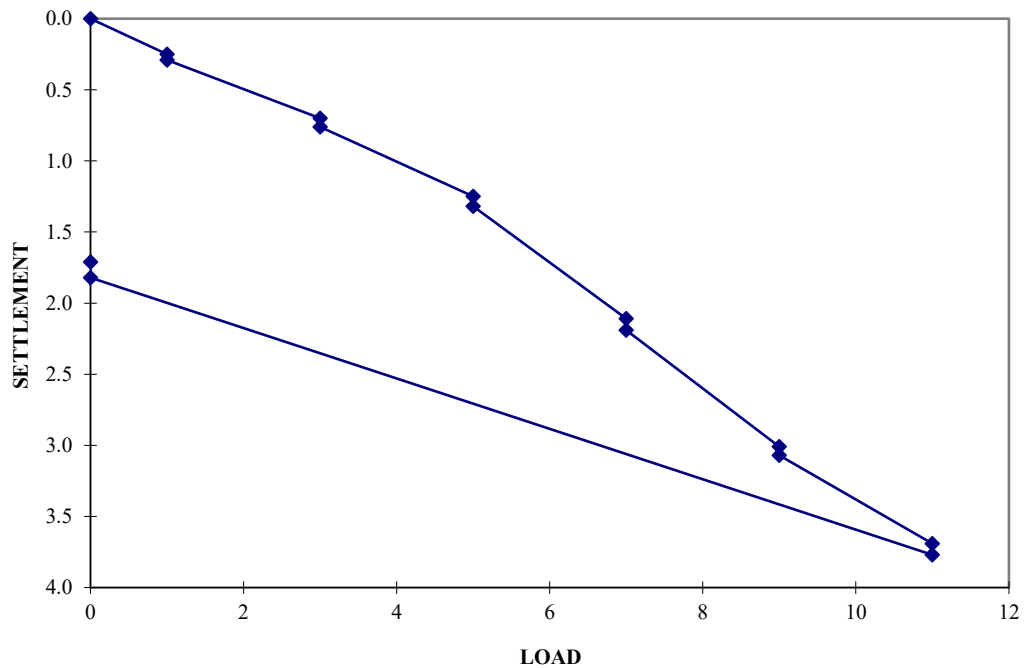

SHEET		1 of 1	CONTRACT No	233579-01
CONTRACT		Millwood School, Bury	DATE OF TEST	18.08.25
TEST FOOTING SIZE		600mm Dia	INSTALL DATE	15.08.25
COLUMN No		350	TEST DEPTH	200mm
PLOT No		W-site	TEST No	Plt02
TIME	ELAPSED TIME IN HOURS MIN	APPLIED LOAD TONNES		AVERAGE SETTLEMENT MM
10:00	00:00	0		0.00
10:01	00:01	1		0.29
10:05	00:05	1		0.33
10:06	00:06	3		0.65
10:10	00:10	3		0.69
10:11	00:11	5		1.31
10:15	00:15	5		1.36
10:16	00:16	7		2.00
10:20	00:20	7		2.06
10:21	00:21	9		2.70
10:25	00:25	9		2.75
10:26	00:26	11		3.07
10:35	00:35	11		3.13
10:40	00:40	0		1.51
10:45	00:45	0		1.44


PLATE LOAD TEST

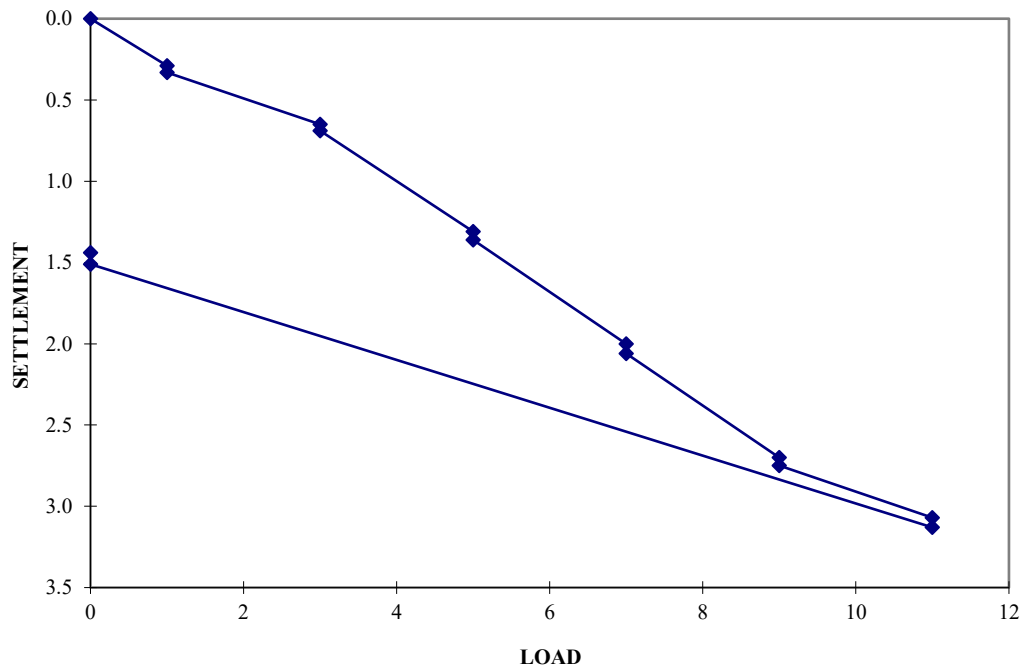

SHEET		1 of 1	CONTRACT No	233579-01
CONTRACT		Millwood School, Bury	DATE OF TEST	18.08.25
TEST FOOTING SIZE		600mm Dia	INSTALL DATE	18.08.25
COLUMN No		337	TEST DEPTH	200mm
PLOT No		W-site	TEST No	Plt03

TIME	ELAPSED TIME IN HOURS MIN	APPLIED LOAD TONNES		AVERAGE SETTLEMENT MM	
13:30	00:00	0		0.00	
13:31	00:01	1		0.22	
13:35	00:05	1		0.26	
13:36	00:06	3		0.54	
13:40	00:10	3		0.59	
13:41	00:11	5		0.99	
13:45	00:15	5		1.05	
13:46	00:16	7		1.70	
13:50	00:20	7		1.74	
13:51	00:21	9		2.34	
13:55	00:25	9		2.39	
13:56	00:26	11		3.09	
14:05	00:35	11		3.16	
14:10	00:40	0		1.51	
14:15	00:45	0		1.46	


PLATE LOAD TEST

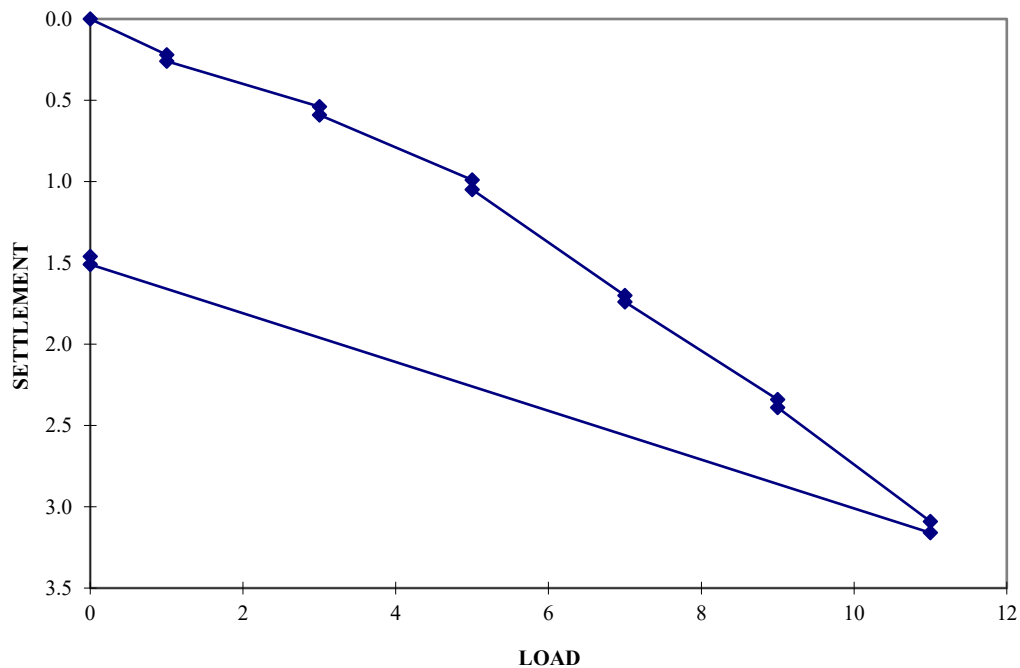

SHEET		1 of 1	CONTRACT No	233579-01
CONTRACT		Millwood School, Bury	DATE OF TEST	19.08.25
TEST FOOTING SIZE		600mm Dia	INSTALL DATE	15.08.25
COLUMN No		88	TEST DEPTH	350mm
PLOT No		W-site	TEST No	Plt04

TIME	ELAPSED TIME IN HOURS MIN	APPLIED LOAD TONNES		AVERAGE SETTLEMENT MM	
10:00	00:00	0		0.00	
10:01	00:01	1		0.41	
10:05	00:05	1		0.43	
10:06	00:06	3		1.05	
10:10	00:10	3		1.08	
10:11	00:11	5		1.95	
10:15	00:15	5		1.99	
10:16	00:16	7		2.79	
10:20	00:20	7		2.82	
10:21	00:21	9		3.45	
10:25	00:25	9		3.47	
10:26	00:26	11		3.94	
10:35	00:35	11		3.97	
10:40	00:40	0		1.82	
10:45	00:45	0		1.73	


PLATE LOAD TEST

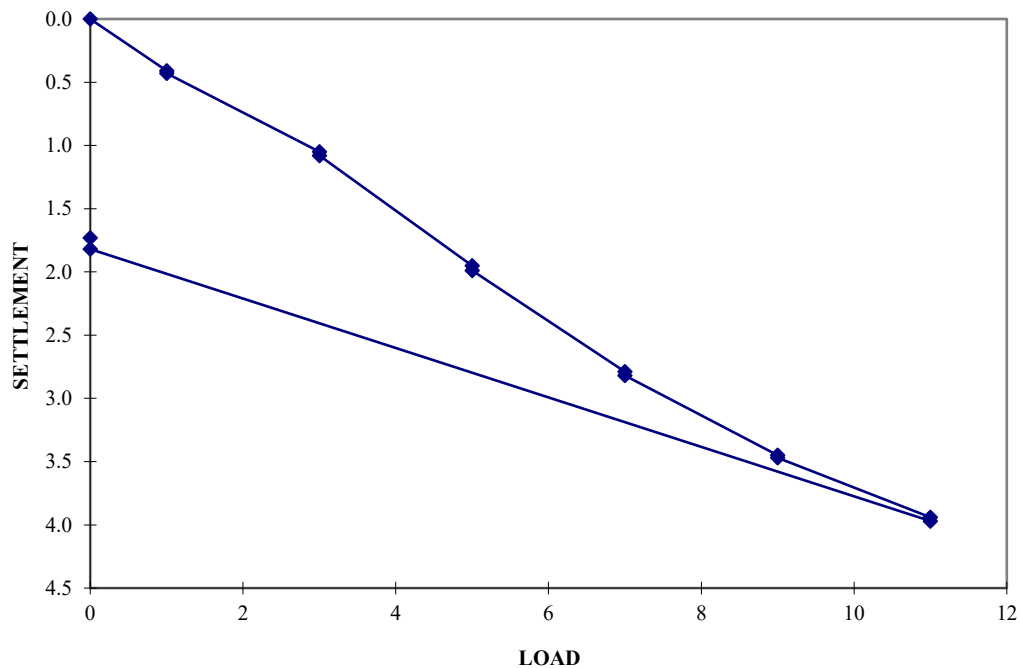

SHEET		1 of 1	CONTRACT No	233579-01
CONTRACT		Millwood School, Bury	DATE OF TEST	19.08.25
TEST FOOTING SIZE		600mm Dia	INSTALL DATE	19.08.25
COLUMN No		290	TEST DEPTH	200mm
PLOT No		W-site	TEST No	Plt05

TIME	ELAPSED TIME IN HOURS MIN	APPLIED LOAD TONNES		AVERAGE SETTLEMENT MM	
13:30	00:00	0		0.00	
13:31	00:01	1		0.32	
13:35	00:05	1		0.37	
13:36	00:06	3		0.85	
13:40	00:10	3		0.90	
13:41	00:11	5		1.31	
13:45	00:15	5		1.36	
13:46	00:16	7		2.02	
13:50	00:20	7		2.08	
13:51	00:21	9		3.02	
13:55	00:25	9		3.07	
13:56	00:26	11		3.74	
14:05	00:35	11		3.81	
14:10	00:40	0		1.77	
14:15	00:45	0		1.68	


PLATE LOAD TEST

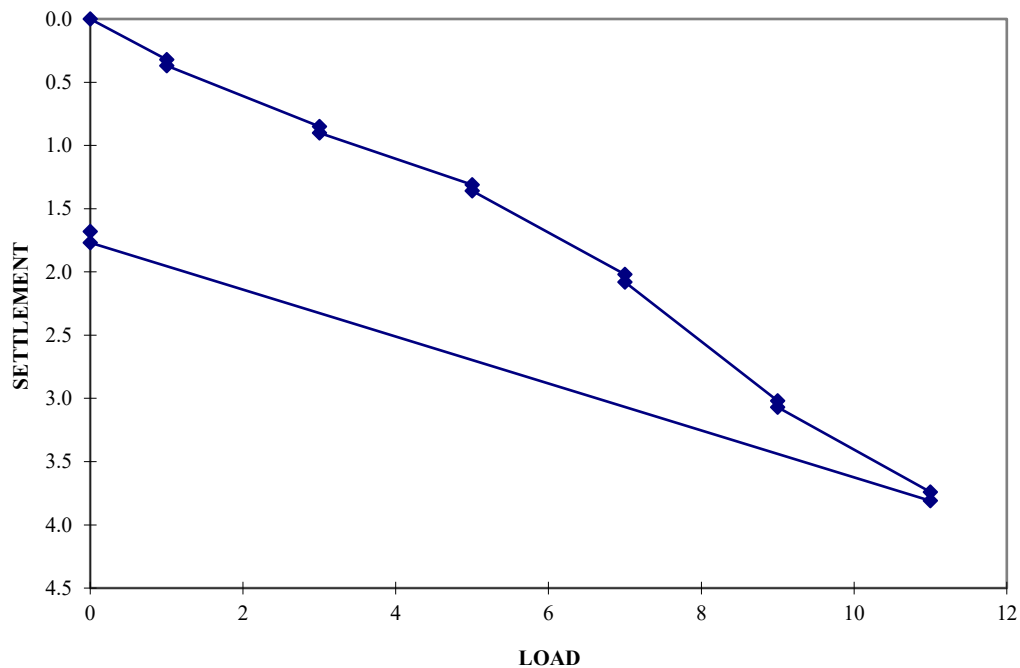

SHEET		1 of 1	CONTRACT No	233579-01
CONTRACT		Millwood School, Bury	DATE OF TEST	20.08.25
TEST FOOTING SIZE		600mm Dia	INSTALL DATE	20.05.25
COLUMN No		157	TEST DEPTH	250mm
PLOT No		W-site	TEST No	Plt06


TIME	ELAPSED TIME IN HOURS MIN	APPLIED LOAD TONNES		AVERAGE SETTLEMENT MM	
09:30	00:00	0		0.00	
09:31	00:01	1		0.43	
09:35	00:05	1		0.48	
09:36	00:06	3		0.78	
09:40	00:10	3		0.83	
09:41	00:11	5		1.51	
09:45	00:15	5		1.57	
09:46	00:16	7		2.31	
09:50	00:20	7		2.35	
09:51	00:21	9		3.18	
09:55	00:25	9		3.24	
09:56	00:26	11		4.00	
10:05	00:35	11		4.06	
10:10	00:40	0		1.99	
10:15	00:45	0		1.87	

PLATE LOAD TEST

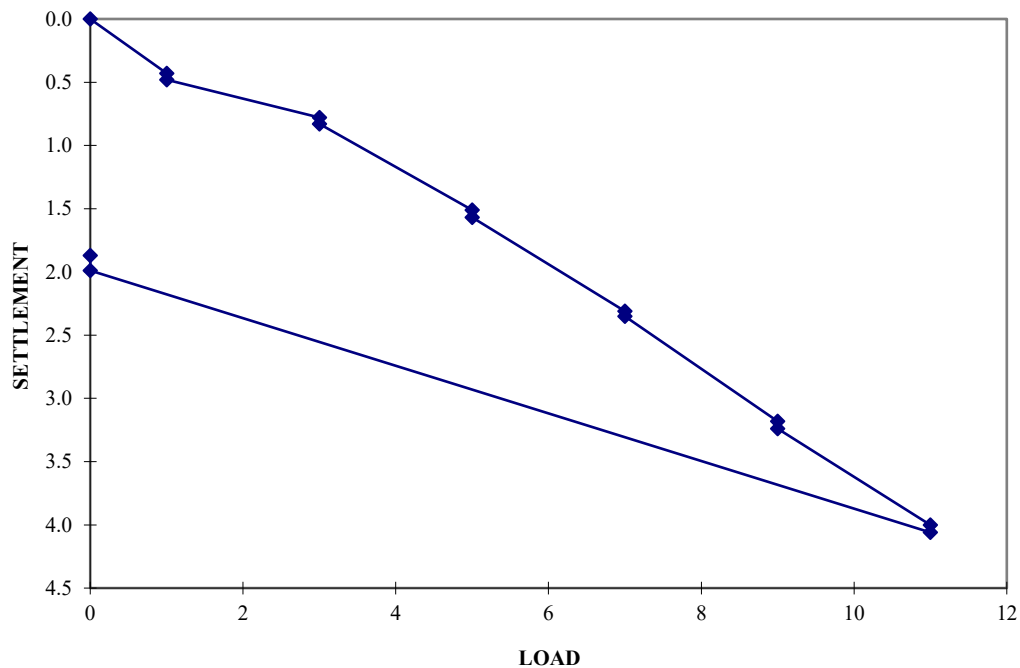

SHEET		1 of 1	CONTRACT No	233579-01
CONTRACT		Millwood School, Bury	DATE OF TEST	18.08.25
TEST FOOTING SIZE		1.5 x 600mm	INSTALL DATE	15.08.25
COLUMN No		142-143	TEST DEPTH	350mm
PLOT No		W-Site	TEST No	DF01
TIME	ELAPSED TIME IN HOURS MIN	APPLIED LOAD TONNES		AVERAGE SETTLEMENT MM
16:00	00:00	0		0.00
16:05	00:05	2		0.15
16:30	00:30	2		0.24
16:35	00:35	4		0.65
17:00	01:00	4		0.73
17:05	01:05	6		1.42
17:30	01:30	6		1.51
17:35	01:35	8		2.21
18:00	02:00	8		2.29
18:05	02:05	10		3.02
18:30	02:30	10		3.12
18:35	02:35	12		3.82
19:00	03:00	12		3.91
19:05	03:05	14		4.25
19:30	03:30	14		4.33
07:00	15:00	14		4.41
07:05	15:05	0		2.11
07:40	15:40	0		2.00

DUMMY FOOT TEST

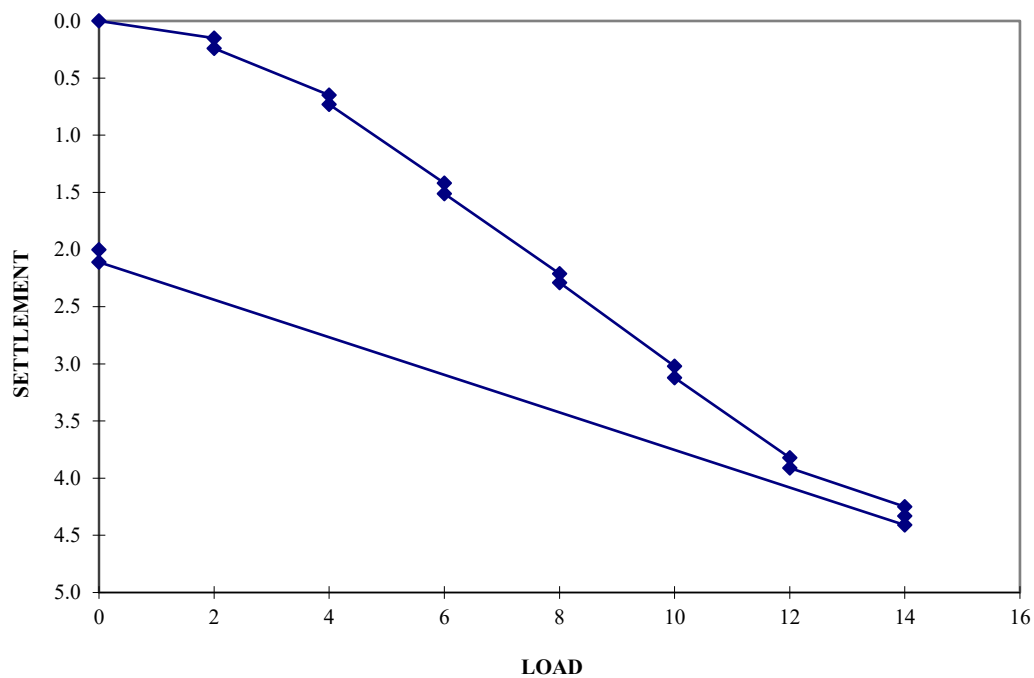

SHEET		1 of 1	CONTRACT No	233579-01
CONTRACT		Millwood School, Bury	DATE OF TEST	20.08.25
TEST FOOTING SIZE		1.5 x 600mm	INSTALL DATE	20.08.25
COLUMN No		207-208	TEST DEPTH	400mm
PLOT No		W-Site	TEST No	DF02
TIME	ELAPSED TIME IN HOURS MIN	APPLIED LOAD TONNES		AVERAGE SETTLEMENT MM
16:30	00:00	0		0.00
16:35	00:05	2		0.52
17:00	00:30	2		0.56
17:05	00:35	4		1.35
17:30	01:00	4		1.40
17:35	01:05	6		2.45
18:00	01:30	6		2.51
18:05	01:35	8		3.46
18:30	02:00	8		3.52
18:35	02:05	10		4.31
19:00	02:30	10		4.36
19:05	02:35	12		4.94
19:30	03:00	12		5.00
19:35	03:05	14		5.41
20:00	03:30	14		5.45
07:00	14:30	14		5.54
07:05	14:35	0		2.59
07:30	15:00	0		2.48

DUMMY FOOT TEST

