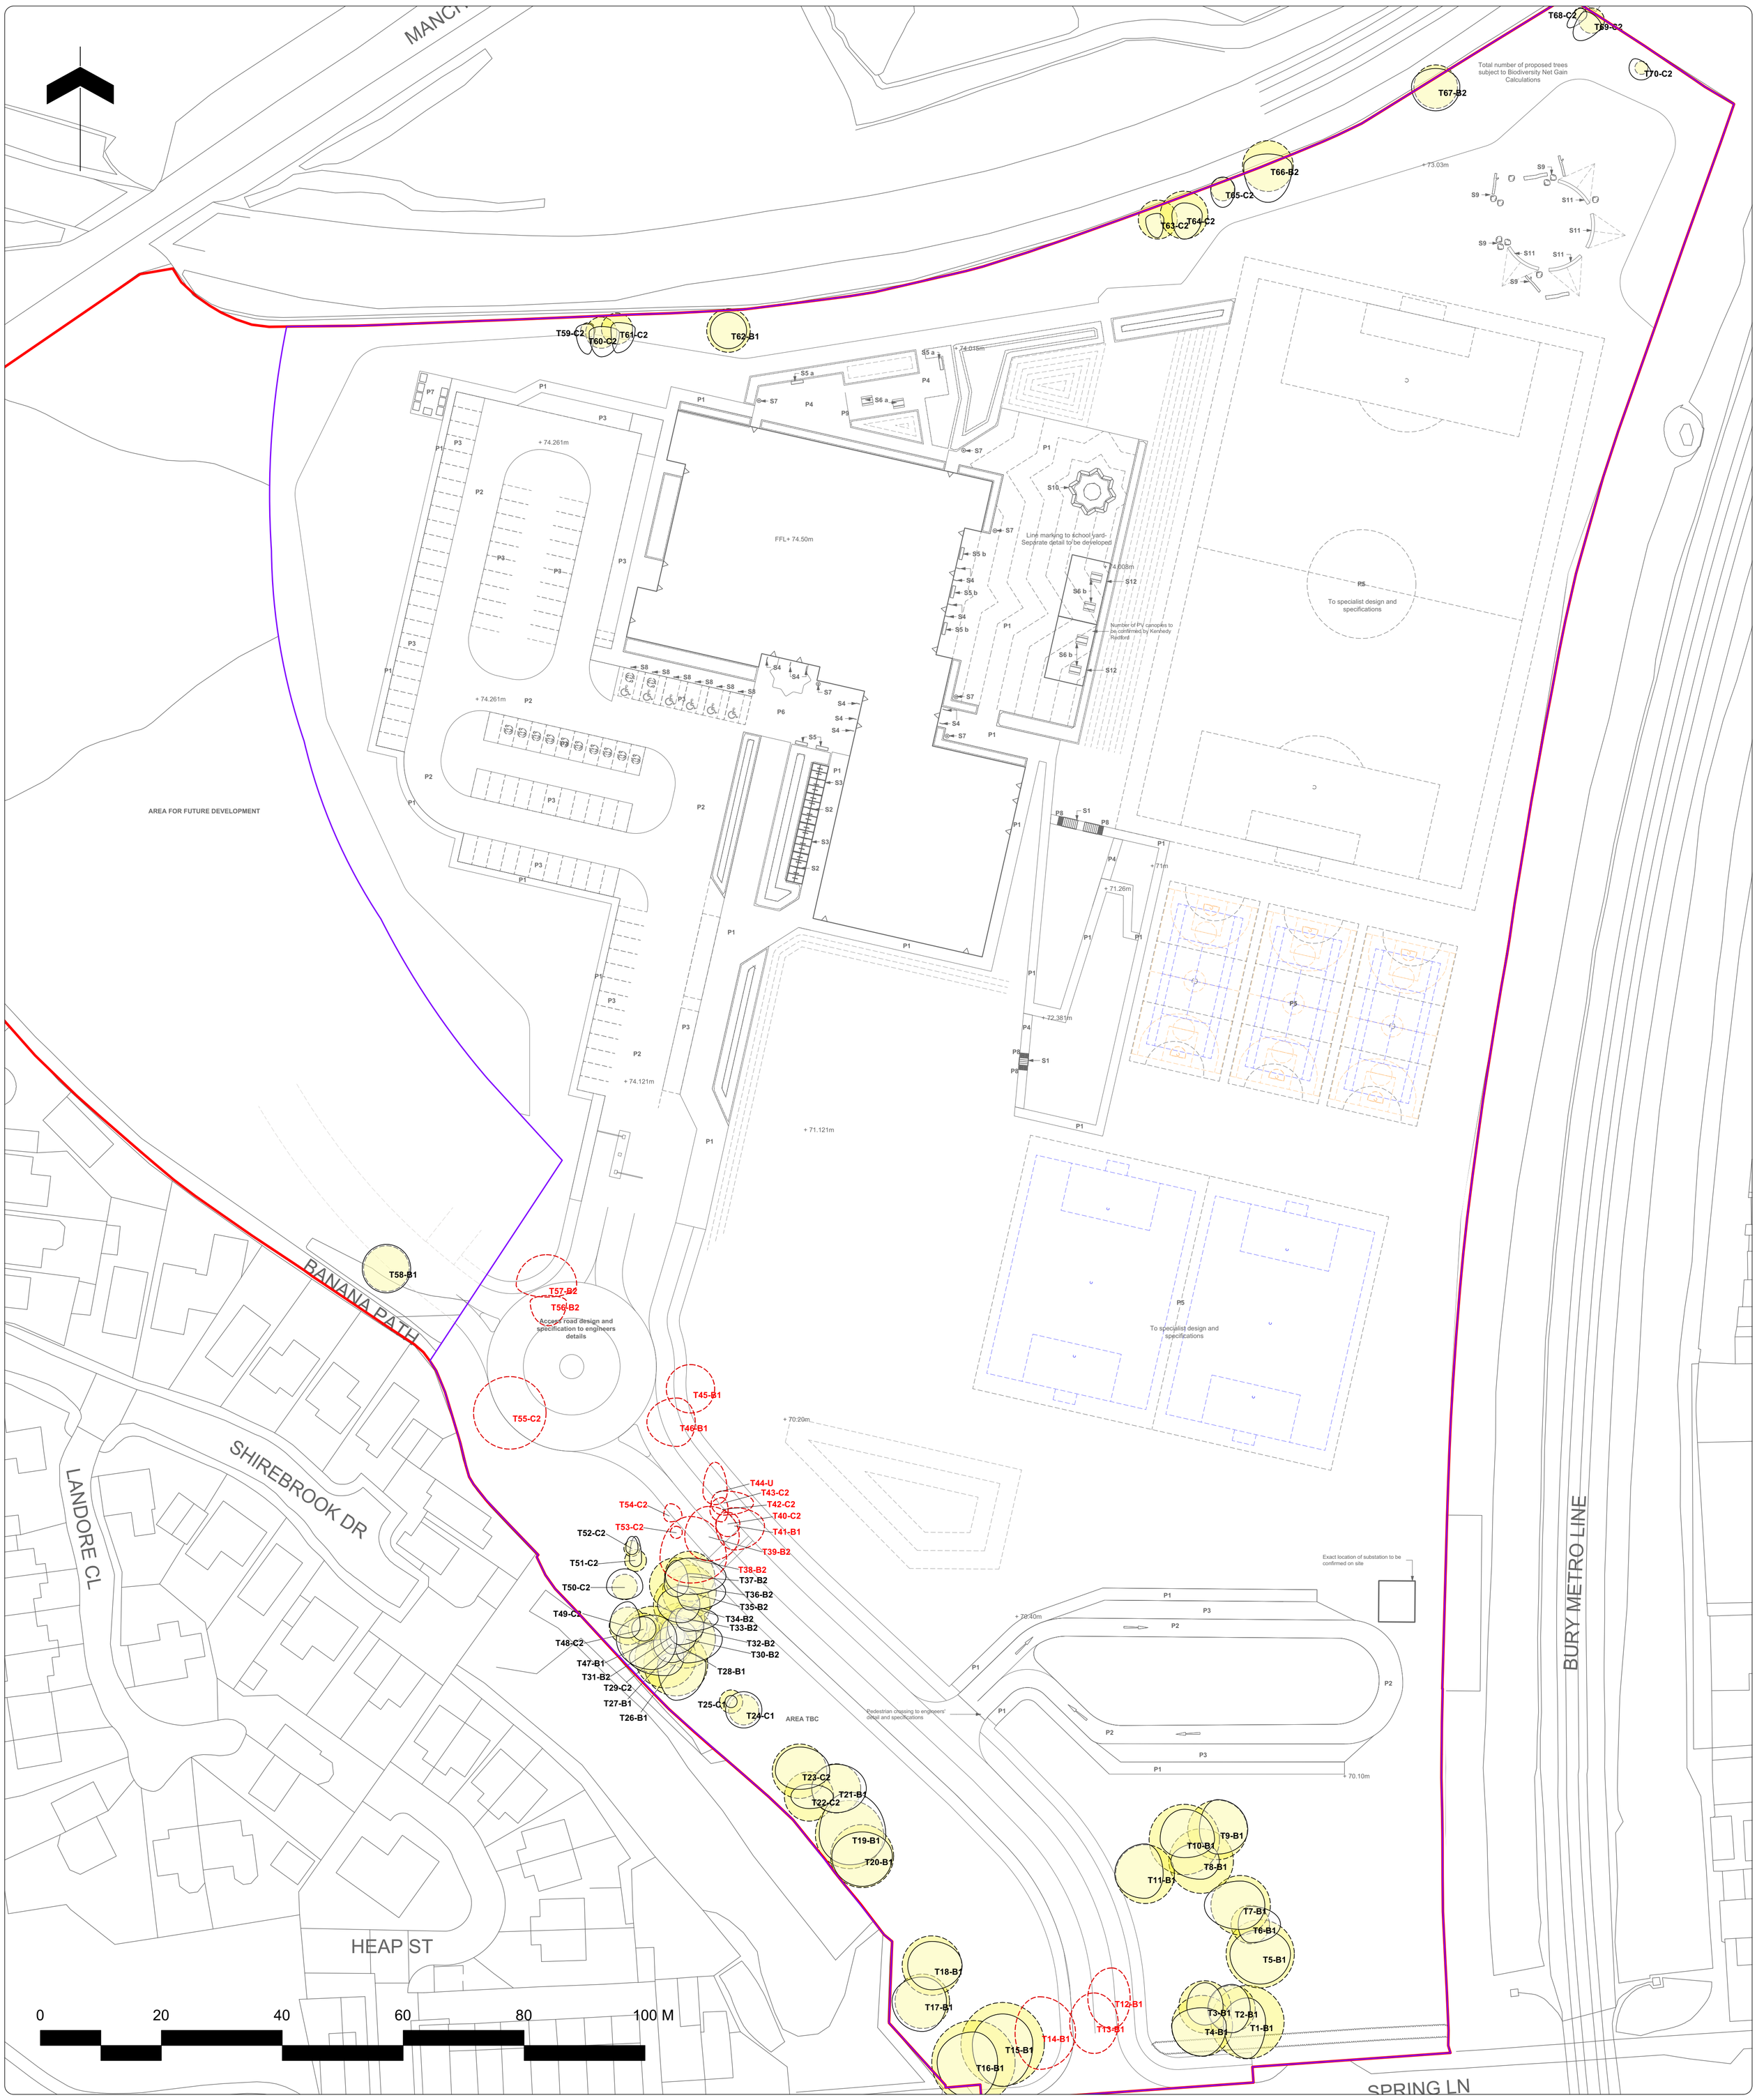

Note

1. Do not scale from this drawing
2. To be read in conjunction with Project Risk Register REF: FS1013-ALA-EX-XX-RR-L-00001
3. To be read in conjunction with all other Landscape Architect's drawings
4. To be read in conjunction with Outline Landscape Specification REF: FS1013-ALA-EX-XX-SP-L-0001

ID	RISK	MITIGATION	DATE MITIGATED
1	Drowning in dry retention basin	2.4m fencing. End user access restricted. Basin to be 600mm deep. Basin is dry except during a stormwater event. Warning sign.	31.07.23
2	Falling on stairs while accessing sport pitches	Stairway is 2m wide. Hand rails provided at standard widths.	31.07.23
3	Collision between pedestrians and vehicles accessing accessible parking bays	School to manage vehicle speed. Bollards added to bays.	31.07.23
4	Collision between pedestrians and vehicles in car park.	Landscape features to stop vehicles from leaving the roads and parking areas. Road markings to clearly denote parking.	31.07.23
5	Collision between pedestrians and cyclist accessing cycle storage facilities	5m wide pedestrian / cycle approach. School to manage speed on site. Clear wayfinding.	31.07.23
6	Coming into contact with underground utilities and services.	Tree pits to be located outside easement areas. Woodland planting also outside of easement areasgrass/meadow seed only.	31.07.23
7	Falling from height - 1:3 grassed bank to east of sports hall	Grassed banks designed to be to a gradient of max 1:3. 1.1m post and rail timber fencing introduced.	31.07.23
8	Collision between pedestrians and open windows	Green buffers to window openings	31.07.23

RESIDUAL PROJECT RISKS

KEY

As shown in Preliminary Arboricultural Impact Assement. (Please refer to BS 5837: 2012 Preliminary Tree Survey Report prepared by Amnity Tree Arboricultural Consultants REF FS1013-ATC-XX-XX-T-F-0001)

Vegetation removal is recommended outside of the main breeding season (October – February) It is recommended that supervised checks are carried out prior to tree removal by a suitably qualified ecologist.

- Planning Application Boundary
- Extent of Works
- T1 Tree to be retained
- T1 Tree to be removed as a result of proposal
- Tree Root Protection Area (RPA)

Trees Removal Schedule

Tree Reference	Species (Common Name)	Category	Action / Comments
T12	Ash	B1	Removed for Construction.
T13	Norway Maple	B1	Removed for Construction
T14	Norway Maple	B2	Removed for Construction
T38	Ash	B2	Removed for Construction
T39	Norway Maple	B2	Removed for Construction
T40	Hazel	C2	Removed for Construction
T41	Hawthorn	B1	Removed for Construction
T42	Hawthorn	C2	Removed for Construction
T43	Hawthorn	C2	Removed for Construction
T44	Hawthorn	U	Removed following Arboriculturis Recommendation
T45	Hawthorn	B1	Removed for Construction
T46	Ash	B1	Removed for Construction
T53	Hazel	C2	Removed for Construction
T54	Ash	C2	Removed for Construction
T55	Goat Willow	C2	Removed for Construction
T56	Silver Birch	B2	Removed for Construction
T57	Common Oak	B2	Removed for Construction

DfE DESIGN DELIVERABLE REF :
757

DATE	REV	DESCRIPTION OF REVISION	DRAWN BY	APPROVED BY
07/09/2023	P02	Issued for Planning	PH	BS
11/08/2023	P01	Issued for ITT	PH	BS

REVISIONS

STATUS :
S2 - *For Planning*

ares LANDSCAPE ARCHITECTS
Ares Landscape Architects LTD
Gatecrasher,
51 Eyre Lane
Sheffield
S1 4RB
t: 0114 276 2000
e: hello@aresdesign.co.uk
w: ares.eu.com

CLIENT :
Morgan Sindall

PROJECT TITLE :
Star Radcliffe Academy, Bury

DRAWING TITLE :
Tree retention and removal plan

DRAWING SCALE :	DRAWN BY :	DRAWN DATE :
1:500	PH	06/07/2023
PAPER SIZE :	APPROVED BY :	ALA PROJECT CODE:
A1	BS	ALA805

DRAWING NUMBER :	STATUS :	REVISION :
FS1013-ALA-EX-ZZ-D-L-0031	S2	P02
