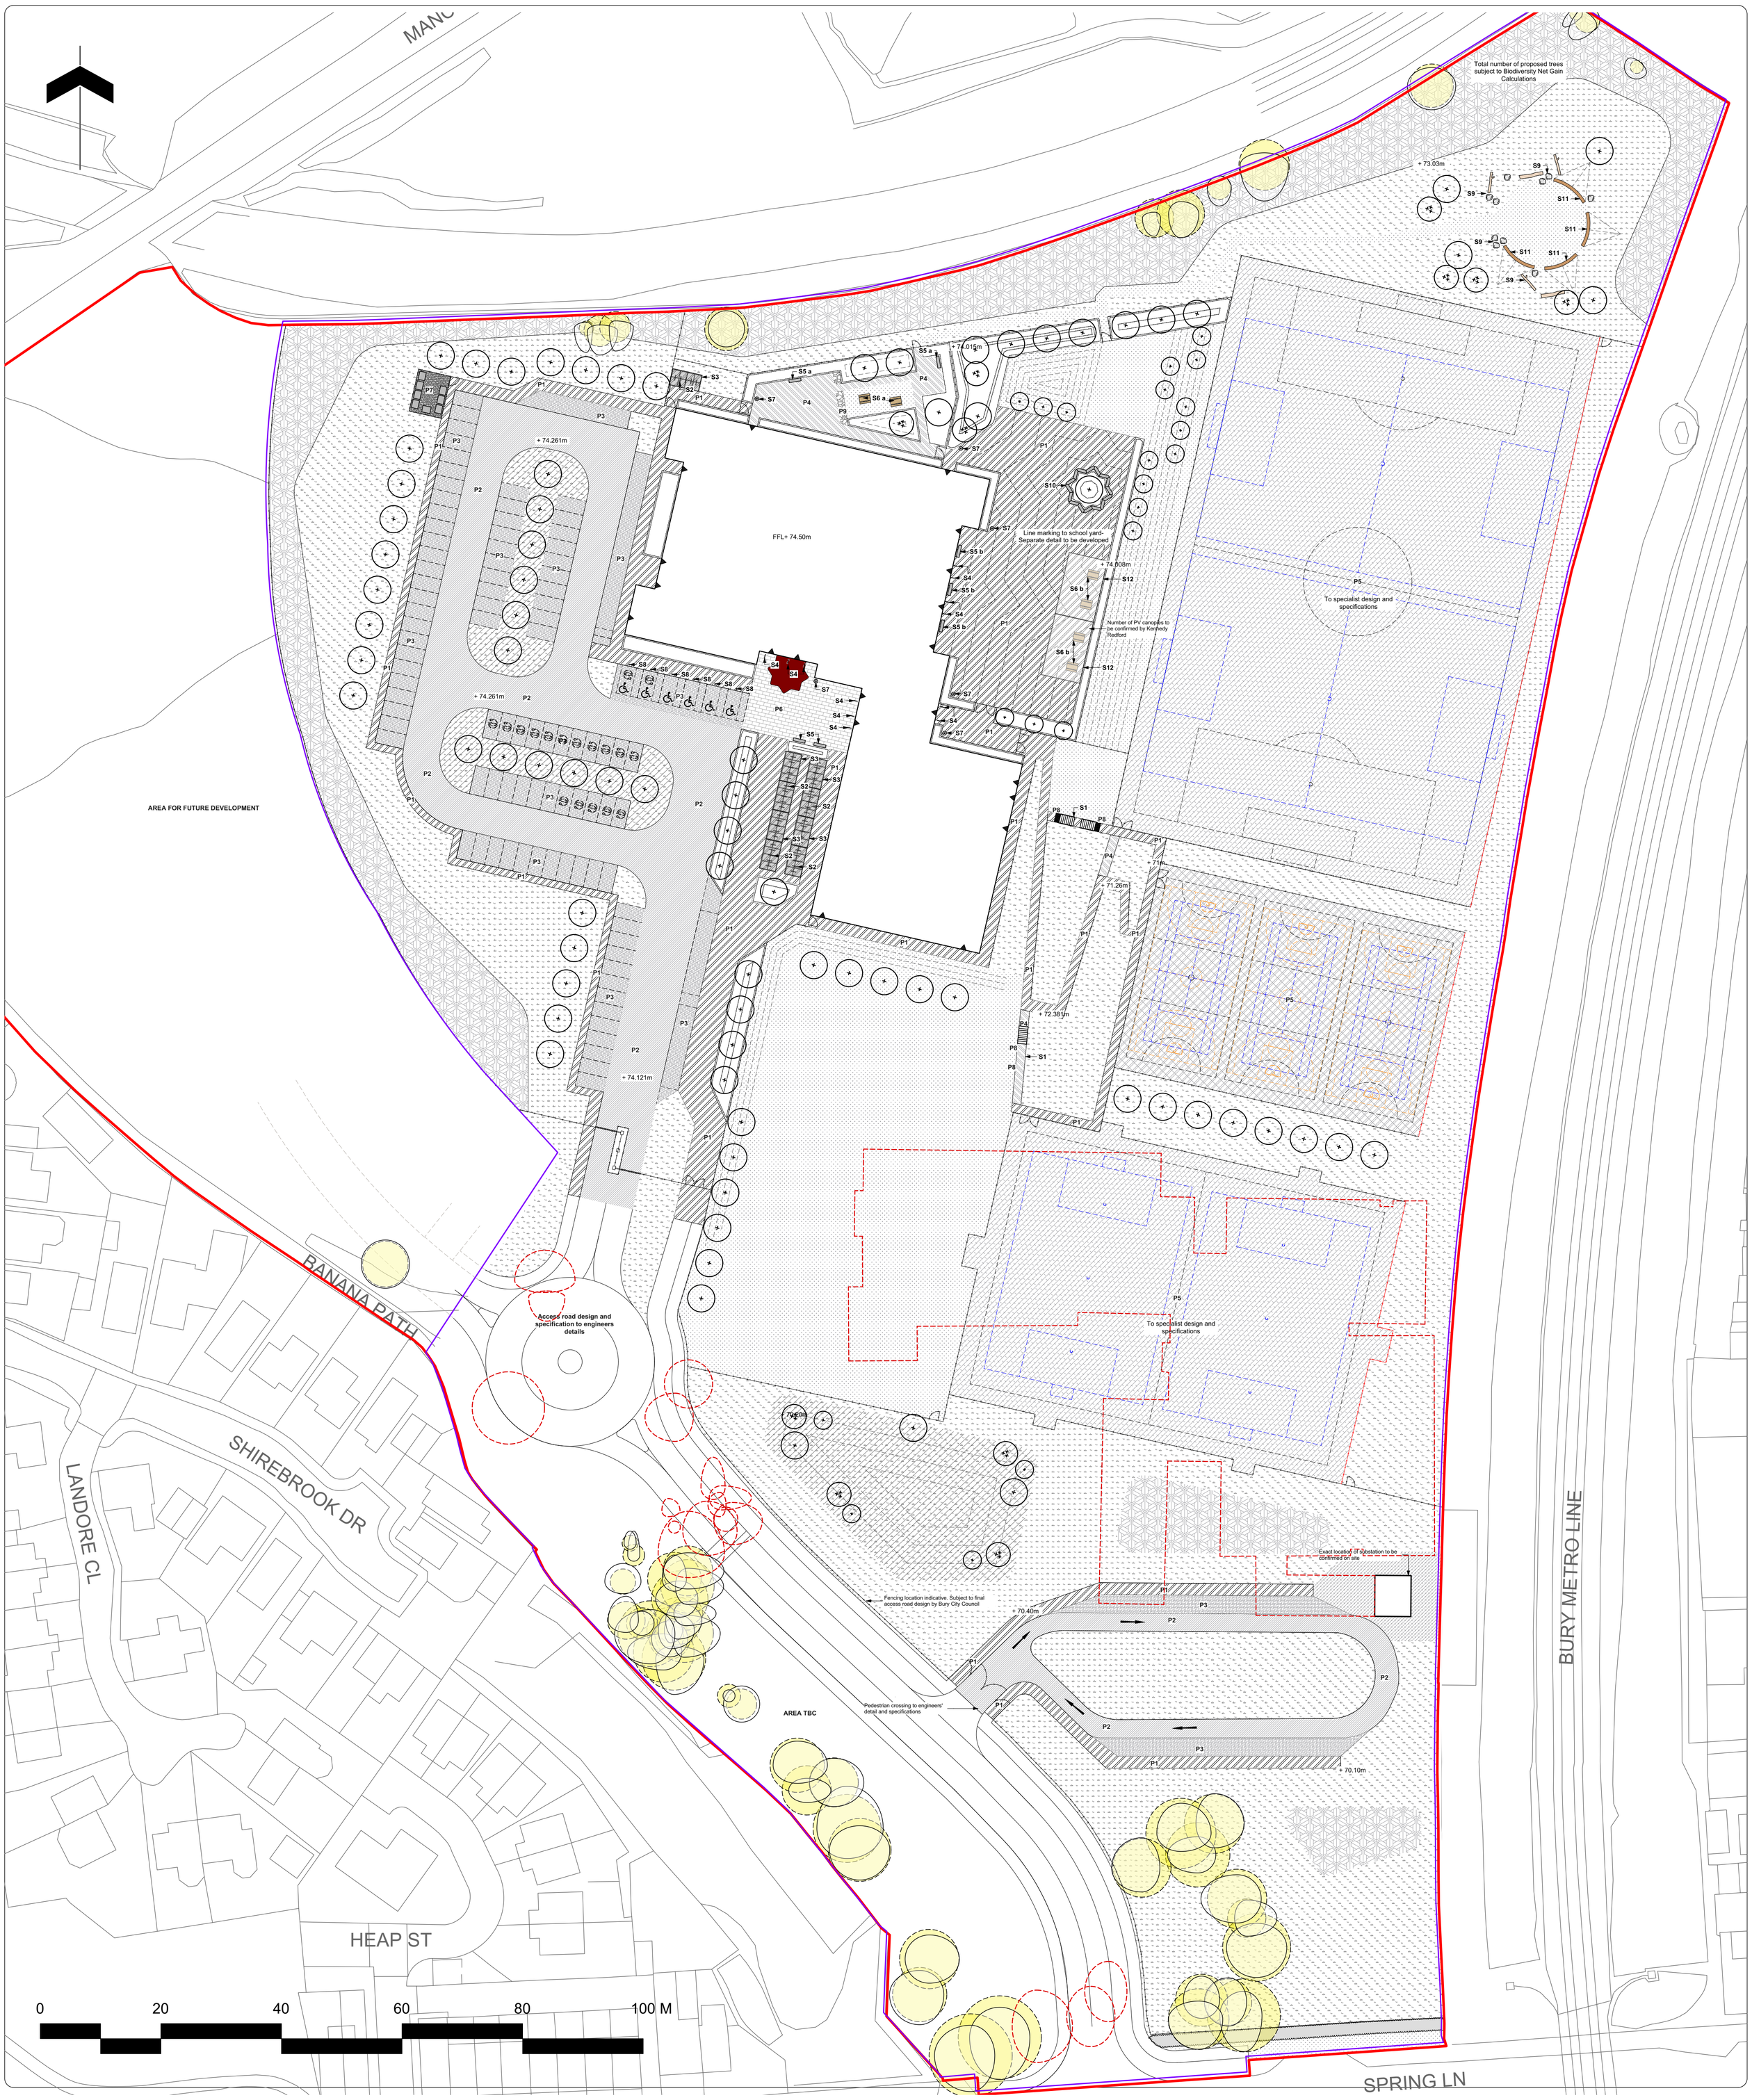


Note

1. Do not scale from this drawing
2. To be read in conjunction with Project Risk Register REF: FS1013-ALA-EX-XX-RR-L-00001
3. To be read in conjunction with all other Landscape Architect's drawings
4. To be read in conjunction with Outline Landscape Specification REF: FS1013-ALA-EX-XX-SP-L-0001

RESIDUAL PROJECT RISKS

ID	RISK	MITIGATION	DATE MITIGATED
1	Drowning in dry retention basin	2.4m fencing. End user access restricted. Basin to be 600mm deep. Basin is dry except during a stormwater event. Warning sign.	31.07.23
2	Falling on stairs while accessing sport pitches	Stairway is 2m wide. Hand rails provided at standard widths.	31.07.23
3	Collision between pedestrians and vehicles accessing accessible parking bays	School to manage vehicle speed. Bollards added to bays.	31.07.23
4	Collision between pedestrians and vehicles in car park.	Landscape features to stop vehicles from leaving the roads and parking areas. Road markings to clearly dencote parking.	31.07.23
5	Collision between pedestrians and cyclist accessing cycle storage facilities	5m wide pedestrian / cycle approach. School to manage speed on site. Clear wayfinding.	31.07.23
6	Coming into contact with underground utilities and services.	Tree pits to be located outside easement areas. Woodland planting also outside of easement areasgrass/meadow seed only.	31.07.23
7	Falling from height - 1:3 grassed bank to east of sports hall	Grassed banks designed to be to a gradient of max 1:3. 1.1m post and rail timber fencing introduced.	31.07.23
8	Collision between pedestrians and open windows	Green buffers to window openings	31.07.23

KEY

Site

- Planning Application Boundary
- Extent of Works
- Proposed Building
- Existing Building to be demolished
- Existing Tree Retained
- Root Protection Area (RPA)
- Existing Tree to be removed
- Propsed Contours

Planting

Details refer to Planting Plan

- Proposed Tree
- Proposed Multi-stem Tree
- Grass Seed
- Amenity Planting
- Meadow Planting
- Swale Meadow Planting
- Woodland Planting
- Artificial Turf
- Hedge

Hard Surfaces

- P1 Pedestrian Macadam — To Engineer's Specification
- P2 Vehicular Macadam — To Engineer's Specification
- P3 Permeable Concrete Block Paving — Refer to School Specific Outline Specification for Details
- P4 Coloured Pedestrian Macadam — To Engineer's Specification
- P5 MUGA Permeable Surface — To Engineer's Specification
- P6 Concrete Block Paving — Refer to School Specific Outline Specification for Details
- P7 Concrete Surfacing — To Engineer's Specification
- P8 Corduroy Tactile Paving — Refer to School Specific Outline Specification for Details
- P9 Sensory Trail — Refer to School Specific Outline Specification for Details

Furniture

- S1 Steps and Handrails — Refer to School Specific Outline Specification for Details
- S2 Cycle Stands — Refer to School Specific Outline Specification for Details
- S3 Cycle Shelter — Refer to School Specific Outline Specification for Details
- S4 Door Protection Barrier — Refer to School Specific Outline Specification for Details
- S5 Seating Bench — Refer to School Specific Outline Specification for Details
- S6 Picnic Table — Refer to School Specific Outline Specification for Details
- S7 Litter Bin — Refer to School Specific Outline Specification for Details
- S8 Bollards — Refer to School Specific Outline Specification for Details
- S9 Ecological Enhancement Features — Refer to School Specific Outline Specification for Details
- S10 Bespoke Star Seating — Refer to School Specific Outline Specification for Details
- S11 Seating to habitat area — Refer to School Specific Outline Specification for Details
- S12 PV Canopy — Refer to School Specific Outline Specification for Details

Fencing and Structures

- Proposed Fencing & Gates — Refer to Fencing General Arrangement for Details

DfE DESIGN DELIVERABLE REF :

150

REVISIONS

DATE	REV	DESCRIPTION OF REVISION	DRAWN BY	APPROVED BY
13/11/2023	P03	Staff Cycle shelter location revised. 2No. 7-a-side football markings shown within 3G pich, note added to key, Note added to Key regarding informal mini-football markings. Note added to Key regarding EV parking.	BS	-
07/09/2023	P02	Issued for Planning	PH	BS
11/08/2023	P01	Issued for ITT	PH	BS

STATUS :

S2 - *For Planning*

ares LANDSCAPE ARCHITECTS

Ares Landscape Architects LTD
Gatecrasher,
51 Eyre Lane
Sheffield
S1 4RB

t: 0114 276 2000
e: hello@aresdesign.co.uk
w: ares.eu.com

CLIENT :

Morgan Sindall

PROJECT TITLE :

Star Radcliffe Academy, Bury

DRAWING TITLE :

Site Landscaping Plan - Overview

DRAWING SCALE :	DRAWN BY :	DRAWN DATE :
1:500	PH	06/07/2023
PAPER SIZE :	APPROVED BY :	ALA PROJECT CODE:
A1	BS	ALA805

DRAWING NUMBER : **FS1013-ALA-EX-ZZ-D-L-0004** STATUS : **S2** REVISION : **P03**
