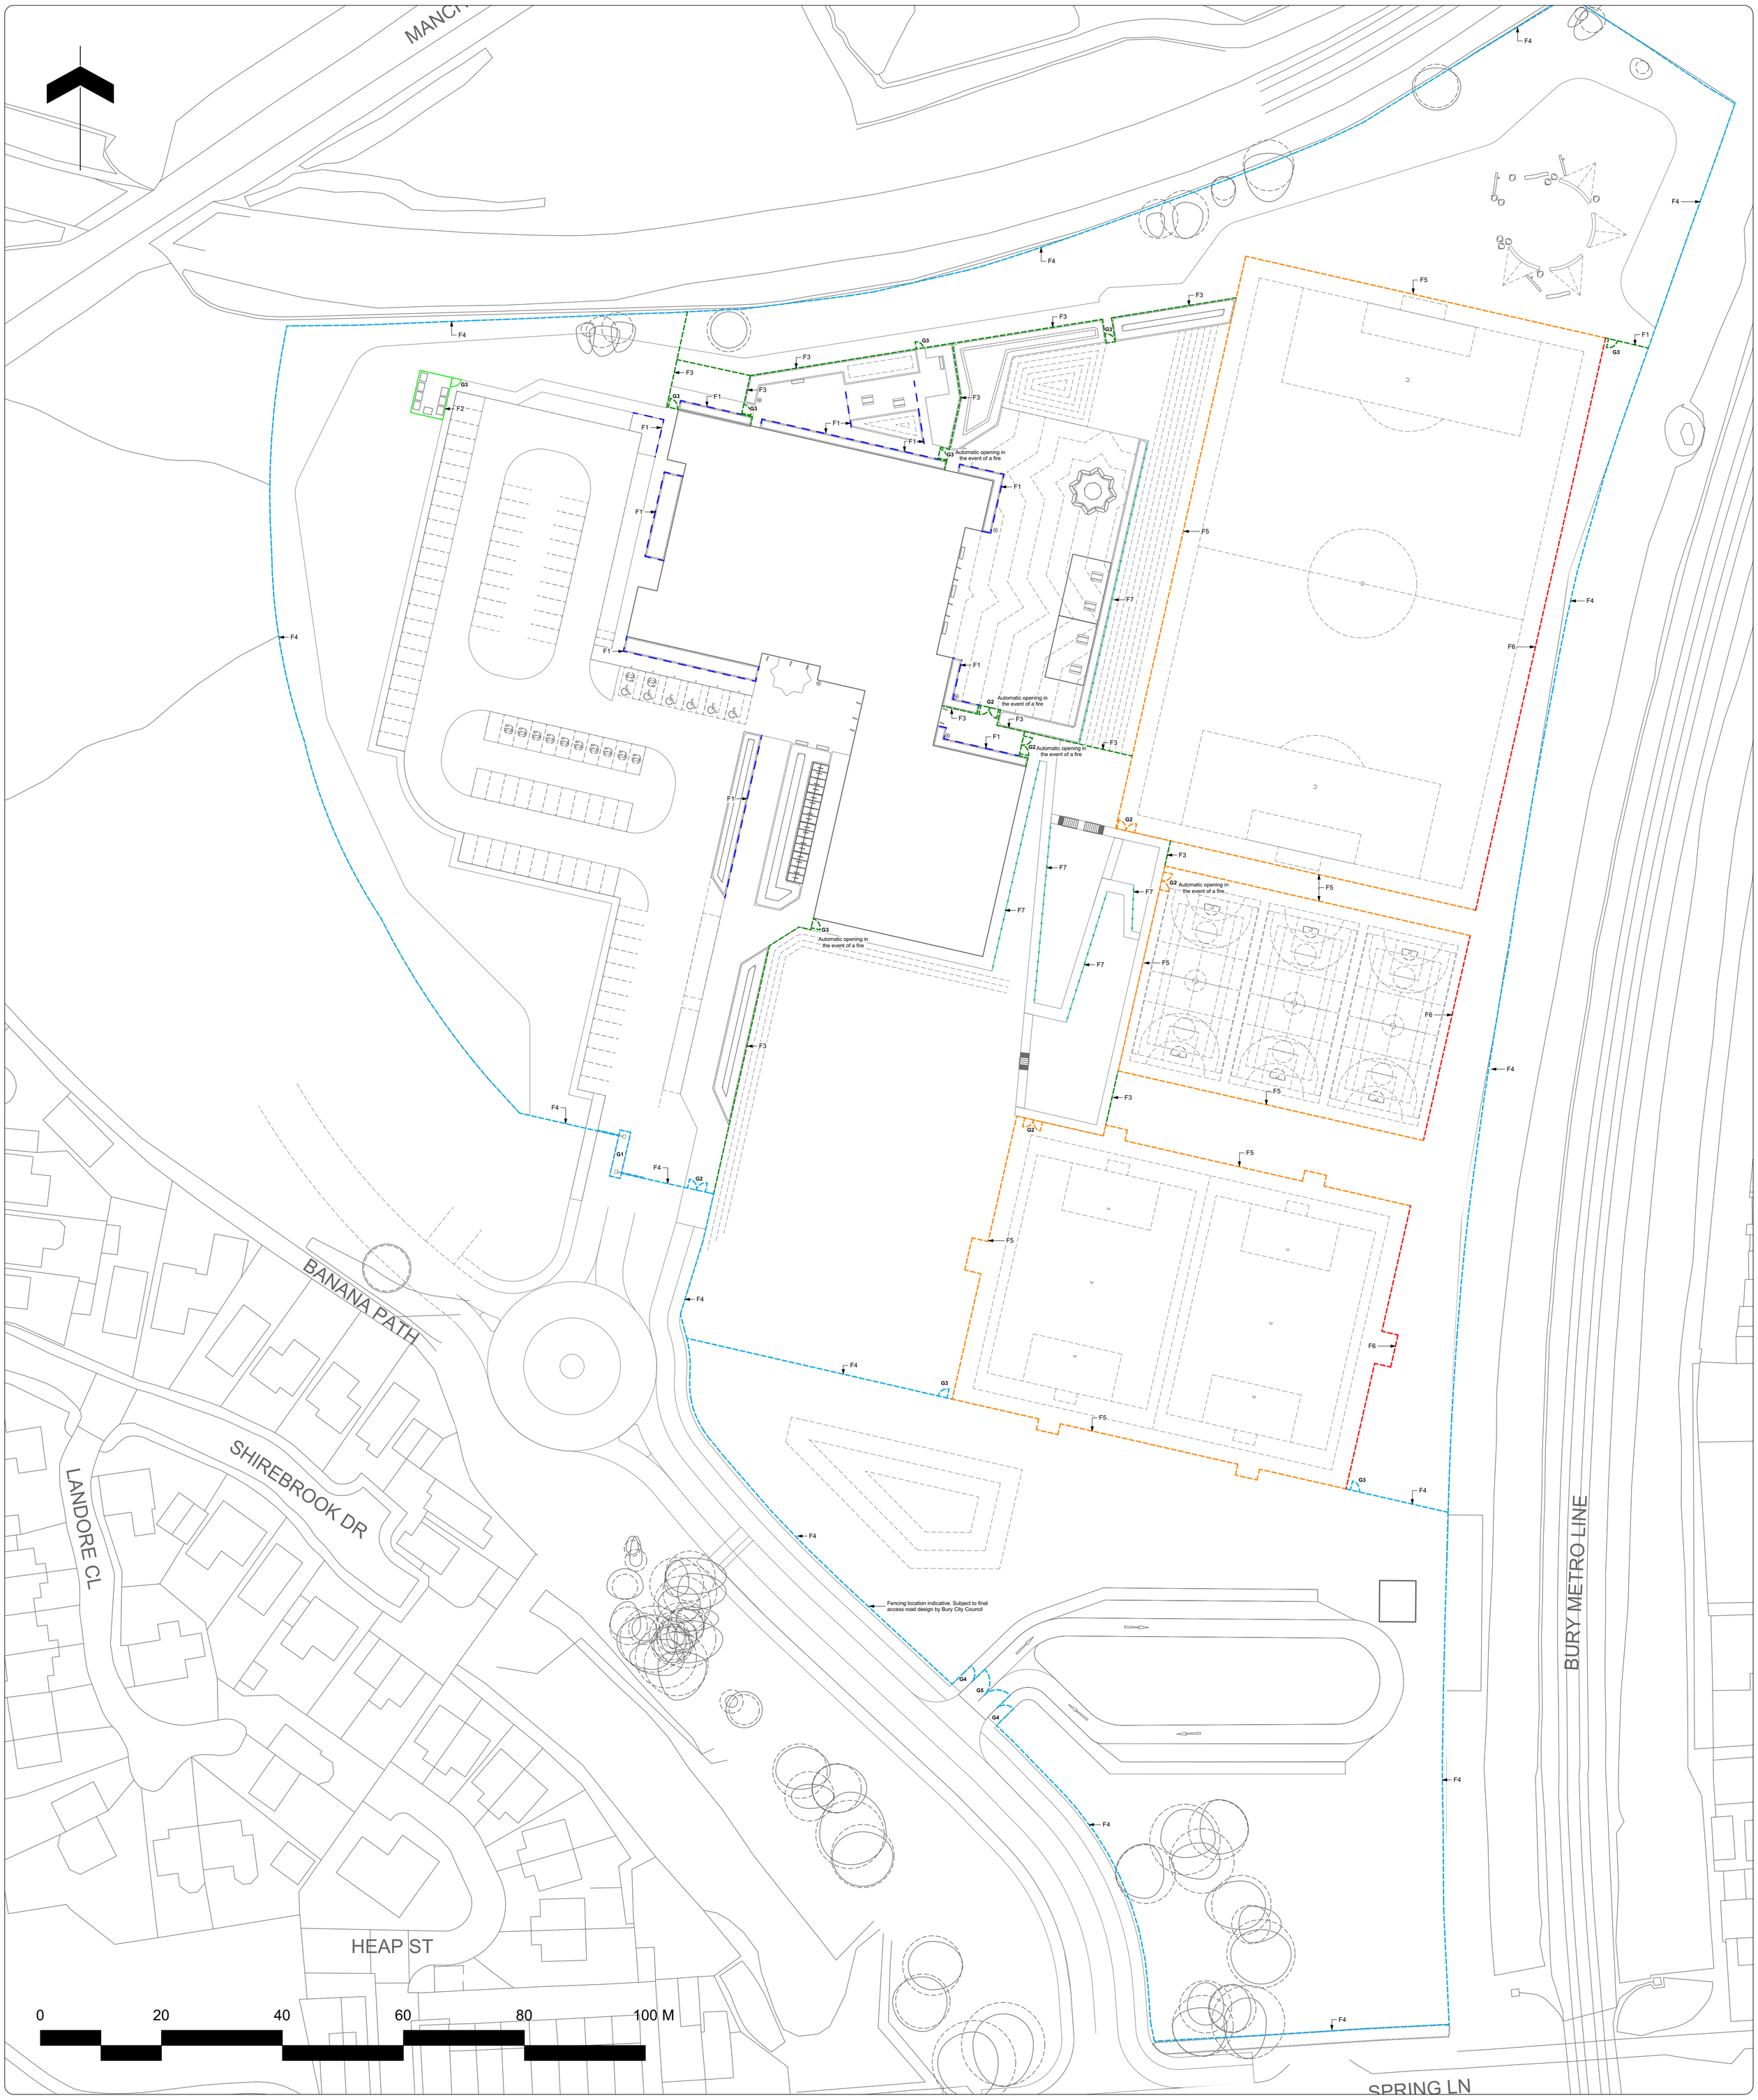


Note

1. Do not scale from this drawing
2. To be read in conjunction with Project Risk Register REF: FS1013-ALA-EX-XX-RR-L-00001
3. To be read in conjunction with all other Landscape Architect's drawings
4. To be read in conjunction with Outline Landscape Specification REF: FS1013-ALA-EX-XX-SP-L-0001

ID	RISK	MITIGATION	DATE MITIGATED
1	Drowning in dry retention basin	2.4m fencing. End user access restricted. Basin to be 600mm deep. Basin is dry except during a stormwater event. Warning sign.	31.07.23
2	Falling on stairs while accessing sport pitches	Stairway is 2m wide. Hand rails provided at standard widths.	31.07.23
3	Collision between pedestrians and vehicles accessing accessible parking bays	School to manage vehicle speed. Bollards added to bays.	31.07.23
4	Collision between pedestrians and vehicles in car park.	Landscape features to stop vehicles from leaving the roads and parking areas. Road markings to clearly denote parking.	31.07.23
5	Collision between pedestrians and cyclist accessing cycle storage facilities	5m wide pedestrian / cycle approach. School to manage speed on site. Clear wayfinding.	31.07.23
6	Coming into contact with underground utilities and services.	Tree pits to be located outside easement areas. Woodland planting also outside of easement areasgrass/meadow seed only.	31.07.23
7	Falling from height - 1:3 grassed bank to east of sports hall	Grassed banks designed to be to a gradient of max 1:3. 1.1m post and rail timber fencing introduced.	31.07.23
8	Collision between pedestrians and open windows	Green buffers to window openings	31.07.23

RESIDUAL PROJECT RISKS

KEY

Fencing and Railing Types

Specification refers to School Specific Outline Specification

- Existing Fence
- F1 — Timber Knee Rail, 0.6m Height
- F2 — Timber Close Board Fence, 2.4m Height
- F3 — Weldmesh Fence, Internal Security, 1.8m Height
- F4 — Weldmesh Fence, Perimeter Security, 2.4m Height
- F5 — Weldmesh Fence, Rebound MUGA Fencing, 3.0m Height
- F6 — Weldmesh Fence, Rebound MUGA Fencing with ball stop netting, 3.0m Height Fence with 2.0m Ball stop Net atop
- F7 — Rail and Post Fencing, 1.2m Height

Gate Types

- G1 — Automated Sliding Gate, 4.2m Width, Automatic- Intercom System
- G2 — Double Leaf Gate, 3m Width, Automatic- Intercom System
- G3 — Single Leaf Gate, 1.5m Width, Automatic / Manual Opening
- G4 — Single Leaf Gate, 2.0m Width, Manual Opening
- G5 — Double Leaf Gate, 6.0m Width, Manual Opening
- G6 — Double Leaf Gate, 5.5m Width, Manual Opening

DfE DESIGN DELIVERABLE REF :

156

DATE	REV	DESCRIPTION OF REVISION	DRAWN BY	APPROVED BY
07/09/2023	P02	Issued for Planning	PH	BS
11/08/2023	P01	Issued for ITT	PH	BS

REVISIONS

STATUS :

S2 - *For Planning*

ares LANDSCAPE ARCHITECTS

Ares Landscape Architects LTD
Gatecrasher,
51 Eyre Lane
Sheffield
S1 4RB

t: 0114 276 2000
e: hello@aresdesign.co.uk
w: ares.eu.com

CLIENT :

Morgan Sindall

PROJECT TITLE :

Star Radcliffe Academy, Bury

DRAWING TITLE :

Fencing General Arrangement

DRAWING SCALE :	DRAWN BY :	DRAWN DATE :
1:500	PH	06/07/2023
PAPER SIZE :	APPROVED BY :	ALA PROJECT CODE:
A1	BS	ALA805

DRAWING NUMBER : **FS1013-ALA-EX-ZZ-D-L-0012** STATUS : **S2** REVISION : **P02**
